

PALM BEACH COUNTY *DK/GW 710*  
BOARD OF COUNTY COMMISSIONERS *R2022-0457*  
AGENDA ITEM SUMMARY

Meeting Date: May 3, 2022 ☐ Consent ☒ Regular  
☐ Workshop ☐ Public Hearing

Submitted By: Department of Airports

I. EXECUTIVE BRIEF

Motion and Title: Staff recommends motion to approve:

- (A) Amendment No. 3 to the Construction Manager (CM) at Risk Contract (Contract) with Lebolo Construction Management, Inc. (LCM) for CM at Risk Services for Miscellaneous Airport Improvements for Palm Beach County Department of Airports (Department) in the amount of \$1,518,790.48 and 290 Calendar Days for Work Order SL 04: Federal Inspection Services (FIS) & Building 846 Storm Resiliency Modifications Package 2 at Palm Beach International Airport (PBI); and
- (B) A Budget Transfer of \$518,791 in the Airport's Improvement and Development Fund to provide budget for the project; including a transfer from Reserves in the amount of \$518,791.

**Summary:** The CM at Risk Contract with LCM was approved by the Board on August 20, 2019 (R-2019-1222). The Contract is for two years with three, one-year renewal options for CM at Risk Services for Airport Improvements for the Department. LCM is a Boynton Beach, Florida, based firm. The County has exercised the first one-year renewal option. The contract value to date is \$1,003,615.62. Approval of Amendment No. 3 in the amount of \$1,518,790.48 and 290 Calendar Days will enable LCM to complete Work Order SL 04: FIS & Building 846 Storm Resiliency Modifications Package 2 at PBI. The Department of Airports Administration and Communications Facility (Building 846) is home for essential personnel who remain on Airport property during hurricanes and other emergency events. This project will provide protection to roof top mounted equipment from impact of wind-borne debris and will replace existing HVAC equipment that is nearing its end of service life with new HVAC equipment as well as provide related structural supports for the new HVAC equipment. The project was presented to the Goal Setting Committee on September 9, 2020 and an Affirmative Procurement Initiative (API) of SBE Subcontracting (Minimum of 20%) of which a MBE Segmented Subcontracting Goal of 5% MBEs composed of African American (AA) firms and Hispanic American (HA) firms was applied. The S/MBE subcontracting participation on this work order is 60.6% with 46.8% participation by HA/AA firms. Current cumulative subcontractor S/M/WBE participation for all work orders to-date under this contract including this amendment is 69.6%. Pursuant to changes to Chapter 332, Florida Statutes, effective October 1, 2020, a governing body of a commercial service airport may not approve purchases of contractual services in excess of the Category Five threshold amount of \$325,000 provided in Section 287.017, Florida Statutes, on a consent agenda. This amendment exceeds the threshold amount and must be approved on the regular agenda. Countywide (AH)

**Background and Policy Issues:** In 2019, the Department procured consultant services to identify improvements needed to facilities housing essential County personnel during hurricane and other emergency events. The improvements were separated into multiple packages due to budget and schedule. Storm Resiliency Modifications Package 1 (Package 1), was completed by LCM in 2020 and included the additional protection of impact-resistant fabric shutters to the exterior side of the impact glazing on Building 846. This work order was under \$200,000 and was approved by Contract Review Committee on June 10, 2020. This project includes implementing the recommended improvements at Building 846 and FIS facility at PBI to meet 2017 Florida Building Codes. Storm Resiliency Modifications Package 2 project will provide protection to roof top mounted equipment from impact of wind-borne debris and will replace existing HVAC equipment that is nearing its end of service life with new HVAC equipment as well as provide related structural supports for the new HVAC equipment. Builder's Risk Insurance is required for this scope of work and will be provided by the Contractor prior to the start of construction.

**Attachments:**

1. Amendment No. 3 to CM at Risk Contract with LCM (w/Contract History) – (3 originals)
2. OEBO Schedules
3. Budget Transfer

Recommended By: *[Signature]* 4-1-22  
Department Director Date

Approved By: *[Signature]* 4/13/22  
County Administrator Date

## II. FISCAL IMPACT ANALYSIS

### A. Five Year Summary of Fiscal Impact:

Fiscal Years	2022	2023	2024	2025	2026
Capital Expenditures	\$1,518,791				
Operating Costs					
External Revenues (Grants)					
Program Income (County)					
In-Kind Match (County)					
NET FISCAL IMPACT	\$1,518,791				
# ADDITIONAL FTE POSITIONS (Cumulative)					

Is Item Included in Current Budget?

Yes \_\_\_\_\_ No X

Does this item include the use of federal funds?

Yes \_\_\_\_\_ No X

Budget Account No: Fund 4111 Department 121 Unit A413 Object 6505  
Reporting Category \_\_\_\_\_

### B. Recommended Sources of Funds/Summary of Fiscal Impact:

Approval of this item provides budget for Amendment No. 3 to the Contract with LCM in the amount of \$1,518,790.48. Funding sources consist of Local funds of \$1,518,791; including a transfer from Reserves of \$518,791.

### C. Departmental Fiscal Review:

## III. REVIEW COMMENTS

### A. OFMB Fiscal and/or Contract Development and Control Comments:

Lisa Mark 4/5/22  
OFMB 4/4/22  
4/5/22

Ann S. Jacobson 4/6/22  
Contract Dev. and Control  
4-6-22

### B. Legal Sufficiency:

Anne Welfant 4/6/22  
Assistant County Attorney

### C. Other Department Review:

\_\_\_\_\_  
Department Director

REVISED 11/17

(THIS SUMMARY IS NOT TO BE USED AS A BASIS FOR PAYMENT)





[Department of State](#) / [Division of Corporations](#) / [Search Records](#) / [Search by Entity Name](#) /

## Detail by Entity Name

Florida Profit Corporation

LEBOLO CONSTRUCTION MANAGEMENT, INC.

### Filing Information

<b>Document Number</b>	P00000095039
<b>FEI/EIN Number</b>	65-1055266
<b>Date Filed</b>	10/06/2000
<b>State</b>	FL
<b>Status</b>	ACTIVE

### Principal Address

2100 CORPORATE DRIVE  
BOYNTON BEACH, FL 33426

Changed: 06/21/2005

### Mailing Address

2100 CORPORATE DRIVE  
BOYNTON BEACH, FL 33426

Changed: 06/21/2005

### Registered Agent Name & Address

LEBOLO, RANDALL E  
2100 CORPORATE DRIVE  
BOYNTON BEACH, FL 33426

Name Changed: 04/03/2002

Address Changed: 01/14/2008

### Officer/Director Detail

#### **Name & Address**

Title D

LEBOLO, RANDALL E  
2100 CORPORATE DRIVE  
BOYNTON BEACH, FL 33426

### Annual Reports



Report Year	Filed Date
2020	03/02/2020
2021	03/04/2021
2022	02/24/2022

**Document Images**

<a href="#"><u>07/24/2022 -- ANNUAL REPORT</u></a>	<a href="#">view image in PDF format</a>
<a href="#"><u>03/04/2021 -- ANNUAL REPORT</u></a>	<a href="#">view image in PDF format</a>
<a href="#"><u>03/02/2020 -- ANNUAL REPORT</u></a>	<a href="#">view image in PDF format</a>
<a href="#"><u>02/13/2019 -- ANNUAL REPORT</u></a>	<a href="#">view image in PDF format</a>
<a href="#"><u>01/16/2018 -- ANNUAL REPORT</u></a>	<a href="#">view image in PDF format</a>
<a href="#"><u>01/18/2017 -- ANNUAL REPORT</u></a>	<a href="#">view image in PDF format</a>
<a href="#"><u>02/13/2016 -- ANNUAL REPORT</u></a>	<a href="#">view image in PDF format</a>
<a href="#"><u>01/26/2015 -- ANNUAL REPORT</u></a>	<a href="#">view image in PDF format</a>
<a href="#"><u>02/26/2014 -- ANNUAL REPORT</u></a>	<a href="#">view image in PDF format</a>
<a href="#"><u>03/03/2013 -- ANNUAL REPORT</u></a>	<a href="#">view image in PDF format</a>
<a href="#"><u>01/10/2012 -- ANNUAL REPORT</u></a>	<a href="#">view image in PDF format</a>
<a href="#"><u>02/16/2011 -- ANNUAL REPORT</u></a>	<a href="#">view image in PDF format</a>
<a href="#"><u>01/29/2010 -- ANNUAL REPORT</u></a>	<a href="#">view image in PDF format</a>
<a href="#"><u>03/06/2009 -- ANNUAL REPORT</u></a>	<a href="#">view image in PDF format</a>
<a href="#"><u>01/14/2008 -- ANNUAL REPORT</u></a>	<a href="#">view image in PDF format</a>
<a href="#"><u>04/02/2007 -- ANNUAL REPORT</u></a>	<a href="#">view image in PDF format</a>
<a href="#"><u>01/27/2006 -- ANNUAL REPORT</u></a>	<a href="#">view image in PDF format</a>
<a href="#"><u>06/21/2005 -- ANNUAL REPORT</u></a>	<a href="#">view image in PDF format</a>
<a href="#"><u>04/16/2004 -- ANNUAL REPORT</u></a>	<a href="#">view image in PDF format</a>
<a href="#"><u>03/17/2003 -- ANNUAL REPORT</u></a>	<a href="#">view image in PDF format</a>
<a href="#"><u>04/03/2002 -- ANNUAL REPORT</u></a>	<a href="#">view image in PDF format</a>
<a href="#"><u>02/26/2001 -- ANNUAL REPORT</u></a>	<a href="#">view image in PDF format</a>
<a href="#"><u>10/06/2000 -- Domestic Proxy</u></a>	<a href="#">view image in PDF format</a>

**R2022 0457**

**AMENDMENT NO. 3 TO THE CONTRACT  
BETWEEN  
PALM BEACH COUNTY DEPARTMENT OF AIRPORTS AND  
LEBOLO CONSTRUCTION MANAGEMENT, INC. FOR  
CONSTRUCTION MANAGEMENT SERVICES  
MISCELLANEOUS AIRPORT IMPROVEMENTS PROJECT NO. DOA 18-13**

This Amendment No. 3 to the Contract is made as of the \_\_\_\_ day of MAY 03 2022 2022, by and between Palm Beach County, Florida (COUNTY) and **LEBOLO CONSTRUCTION MANAGEMENT, INC.**, a corporation authorized to do business in the State of Florida, hereinafter referred to as the CONSTRUCTION MANAGER, having its office and principal place of business for this Contract at 2100 Corporate Drive, Boynton Beach, Florida 33426.

WHEREAS, the Owner and Construction Manager acknowledge and agree that the Contract between Owner and **LEBOLO CONSTRUCTION MANAGEMENT, INC** dated August 20, 2019 (R-2019-1222) is in full force and effect and that this merely supplements said Contract; and

WHEREAS, on July 13, 2021, the County entered into Amendment #1 (R-2021-0888) with the CONSTRUCTION MANAGER and that this merely supplements said Contract; and

WHEREAS, on February 8, 2022, the County entered into Amendment #2 (R-2022-0135) with the CONSTRUCTION MANAGER and that this merely supplements said Contract; and

WHEREAS, the parties hereto entered into a Contract between Owner and CONSTRUCTION MANAGER whereby the CONSTRUCTION MANAGER has rendered or will render pre-construction services as specified therein; and

WHEREAS, the parties have negotiated a Guaranteed Maximum Price (GMP), including CONSTRUCTION MANAGER's fees for construction and warranty services and other services as set forth herein and in the Contract; and

WHEREAS, the CONSTRUCTION MANAGER represents that the CONSTRUCTION MANAGER, Subcontractors, material and equipment suppliers have compared and reviewed all general and specific details on the Drawings and that all conflicts, discrepancies, errors and omissions, which are within the commonly accepted knowledge based of a licensed general contractor, subcontractor, trades persons, manufacturers or other parties required to carry out the Work involved in this Amendment, have been corrected or clarified prior to execution of this Amendment to the Contract, and therefore CONSTRUCTION MANAGER warrants that the GMP (exclusive of contingency) includes the cost of correcting all conflicts, discrepancies, errors, or omissions which CONSTRUCTION MANAGER identifies, or should have identified through the exercise of reasonable skill and care, during the pre-construction phase of this Contract; and

WHEREAS, the CONSTRUCTION MANAGER's review and comparison of all Drawings has taken into consideration the total and complete functioning of all systems and therefore the CONSTRUCTION MANAGER represents that the GMP represents the total cost for complete and functional systems including Pre-Construction Services.

NOW THEREFORE, in considerations of the mutual covenants herein contained, and such other good and

valuable consideration, the receipt of which the parties hereby acknowledge, the parties agree to the following terms and conditions:

(1) GUARANTEED MAXIMUM PRICE

Pursuant to Article 2.2 and Article 6 of the Contract between Owner and CONSTRUCTION MANAGER, the parties have agreed to the establishment of a Guaranteed Maximum Price of **\$1,518,790.48** for the construction costs for **Work Order SL 04: FIS & Building 846 Storm Resiliency Modifications Package 2 at Palm Beach International Airport.**

(2) SCHEDULE OF TIME FOR COMPLETION

Pursuant to Article 5.3, CONSTRUCTION MANAGER shall complete the project within the milestones noted in the table below or Liquidated Damages for failure to complete within the contract time or approved extension thereof shall be assessed.

Description	Calendar Days from NTP	Liquidated Damages
Substantial Completion	260	\$1,000/ Cal Day
Final Completion	290	\$0/ Cal Day

(3) Except as specifically amended herein, all other terms and conditions of the Contract shall remain in full force and effect.

(4) Attachments Exhibit A

IN WITNESS WHEREOF, the Board of County Commissioners of Palm Beach County, Florida has made and executed this Amendment on behalf of the COUNTY and CONSTRUCTION MANAGER has hereunto set its hand the day and year above written.

**R2022 0457** MAY 03 2022

**ATTEST:**

**JOSEPH ABRUZZO, CLERK OF THE  
CIRCUIT COURT & COMPTROLLER**


By:   
Deputy Clerk



**PALM BEACH COUNTY, FLORIDA  
A Political Subdivision of the State of Florida  
BOARD OF COUNTY COMMISSIONERS**

By:   
Robert S. Weinroth, Mayor

**APPROVED AS TO FORM  
AND LEGAL SUFFICIENCY**


By:   
County Attorney

**APPROVED AS TO TERMS  
AND CONDITIONS**

By:   
Director of Airports

**WITNESS:**


**FOR CONSTRUCTION MANAGER  
SIGNATURE**

  
Signature

Sebastian Fonnegra

Name (type or print)

**CONSTRUCTION MANAGER:**

  
Signature

Randall E. Lebolo

President

(Corporate Seal)

## **Exhibit A**

- 1. GMP dated March 21, 2022**
- 2. Public Construction Bond**



# GMP



## PALM BEACH COUNTY DEPARTMENT OF AIRPORTS

DOA 18-13 CM@RISK SERVICES for  
MISCELLANEOUS IMPROVEMENTS PROJECTS  
on a CONTINUING CONTRACT BASIS



### GMP

#### SL - 04 FIS \$ BUILDING STORM RESILIENCY MODIFICATIONS PACKAGE 2

WEST PALM BEACH, FL

Monday, March 21 2022  
2021-0024

DOA 18 - 2A SL-04  
Version 4.0

2100 CORPORATE DRIVE  
BOYNTON BEACH, FL 33426  
LEBOLO.COM | CGC-062151





# Table of Contents

---

## **LETTER**

Section A

### **COST SUMMARY**

### **ASSUMPTIONS & CLARIFICATIONS, ALLOWANCES**

Section B

### **CONSTRUCTION PHASE MANAGEMENT FEE**

### **GENERAL CONDITIONS**

Section C

### **REIMBURSABLE GENERAL CONDITIONS**

Section D

### **MINORITY PARTICIPATION REPORT**

Section E

### **SUBCONTRACTOR BIDDING STATUS REPORT**

Section F

### **SCOPE SHEETS**

### **SUBCONTRACTOR PROPOSALS (See Section F Individual Document)**

Section G

### **PUBLIC AD**

Section H

### **DRAWING LOG**

Section I

### **CONSTRUCTION SCHEDULE**

Section J

### **SITE VISIT ATTENDANCE**

### **BID OPENING LOG**

Section K

### **VALUE ANALYSIS / VALUE ENGINEERING REPORT**

### **CONSTRUCTABILITY REPORT**



March 21, 2022

**Ms. Cynthia M. Portnoy**  
PE Project Manager  
Palm Beach County Department of Airports  
846 Palm Beach International Airport  
West Palm Beach, FL 33406-1470  
(561) 471-7411 Direct  
(954) 242-5181 Mobile

**Ref:DOA 18-2A FIS & Building 846 Storm Resiliency Modifications Package 2**  
**West Palm Beach, FL - SL-04**  
**2020-0024**

Ms. Portnoy,

In accordance with Article 2 - Construction Manager's Basic Services, Article 2.1. The PreConstruction Phase we are submitting the GMP V.4 required information in compliance with the 100% CDs requirements for PreConstruction Services.

We look forward, with much enthusiasm to work with you on this project and being your construction resource and team member in its successful completion.

If you have any questions, please call me at my mobile (561) 632-4894 or email me at [sfonnegra@lebolo.com](mailto:sfonnegra@lebolo.com).

Sincerely,

Sebastian Fonnegra  
**Pre-Construction Manager**  
Lebolo Construction Management, Inc.  
[sfonnegra@lebolo.com](mailto:sfonnegra@lebolo.com)



SECTION A

# Cost Summary

## Assumptions & Clarifications

## Allowances





**GMP**

PROJECT NAME:

LEBOLO PROJECT No:

PBIA PROJECT No:

VERSION:

PROPOSAL DATE:

SL-04 FIS & BUILDING 846 STORM RESILIENCY  
MODIFICATIONS PACKAGE 2

2021-0024

DOA 18-2A SL-04

4.0

Monday, March 21, 2022

FORM LCM-PC-01 | 09/21/2021

**SCOPE OF WORK**

2 Roof chiller units replacement  
New Grating over chillers  
Interior (35) VAV replacement  
Interior finishes  
Interior & Exterior S.Steel

PALM BEACH COUNTY DEPARTMENT OF AIRPORTS			SL-04 FIS & BUILDING 846 STORM RESILIENCY MODIFICATIONS PACKAGE 2							
LEBOLO COST CODE	SPEC. COST CODE	DESCRIPTION OF WORK	846 BUILDING	# PROP.	VENDOR	Sub Permit Inc.	BOND REQ.	BOND COST	DEPOSIT	COMMENTS
<b>DIVISION 2</b>		<b>SITE CONSTRUCTION</b>	<b>\$4,594.48</b>							
02-020		Selective Demolition	\$4,594.48	2	All American Ceilings	\$0	N/A	\$0	No	Acoustical Ceiling removal
<b>DIVISION 5</b>		<b>METALS</b>	<b>\$210,788.50</b>							
05-005		Structural Steel Package	\$210,788.50	2	Van Linda Iron		BOND	\$7,128	No	W8 Chiller bench, Joist bottom chord
<b>DIVISION 7</b>		<b>THERMAL /MOISTURE</b>	<b>\$3,000.00</b>							
07-405		Roofing Package	\$3,000.00	0	LEBOLO ESTIMATE	\$0	N/A	\$0	0	Allowance - Patch & Repairs
<b>DIVISION 9</b>		<b>FINISHES</b>	<b>\$67,143.56</b>							
09-105		Drywall & Framing Package	\$30,850.00	1	I.Q. Constructions		N/A	\$0	No	Drywall ceilings
09-205		Acoustical Ceiling Package	\$27,393.56	1	All American Ceilings		N/A	\$0	No	
09-505		Painting Package	\$8,900.00	1	I.Q. Constructions		N/A	\$0	No	Interior drywall ceilings & Steel Patch & Repairs
<b>DIVISION 15</b>		<b>MECHANICAL</b>	<b>\$640,981.83</b>							
15-105		Fire Protection Package	\$3,685.83	1	Johnsons Controls	\$0	N/A	\$0	0	Sprinkler heads relocation
15-205		HVAC Package	\$577,320.00	4	Quantum Mechanical	\$0	BOND	\$11,320	No	(2) Chillers 90T - 35 VAV Boxes
15-235		HVAC Duct Cleaning	\$59,976.00	3	Quantum Mechanical	\$0	BOND	\$1,176	No	
<b>DIVISION 16</b>		<b>ELECTRICAL</b>	<b>\$41,200.00</b>							
16-005		Electrical Package	\$33,600.00	1	Protect Video	\$0	N/A	\$0	No	(2) Chiller Disconnects & 35 VAV connections
16-105		Low Voltage Package	\$2,500.00	0	LEBOLO ESTIMATE	\$0	N/A	\$0	0	Allowance - Antennas service if required
16-020		Lightning Protection	\$5,100.00	2	Bonded Lightning	\$0	N/A	\$0	No	
	<b>2</b>	<b>SUBTOTAL</b>	<b>\$967,708.37</b>			\$0		\$19,624		
90-035	<b>3</b>	<b>Payment &amp; Performance Bond</b>	<b>\$33,869.79</b>							Article 8 Cost of the Work - Bonds
90-025	<b>4</b>	<b>General Liability - On Site</b>	<b>\$5,806.25</b>							Article 8 Cost of the Work - Insurance (Liability, OCP, Hurricane Fund)
90-030	<b>5</b>	<b>Builders Risk Policy</b>	<b>\$7,257.81</b>							Article 8 Cost of the Work - Builders Risk
Div. 17	<b>6</b>	<b>General Requirements (See GR Detail)</b>	<b>\$44,305.40</b>							Article 8 Cost of the Work - Reimbursable General Conditions (labor other than admin and supervision, clean-up, trash removal, tempr power and utilities, surveys, prep shop drawings, as-builts, safety, machinery etc, reproduction, tools)
91-165	<b>6a</b>	<b>Material Cost Escalation Contingency</b>	<b>\$145,156.26</b>							15.0%
17-810		<b>Permits</b>	<b>\$0.00</b>							Building Permit Fee - by owner
		<b>Subtotal Cost of the Work-w/o precon (Items 2-6a)</b>	<b>\$1,204,103.89</b>							
Div. 80	<b>7</b>	<b>Construction Managers Fee - Art 6.4.CM Management - Staffing</b>	<b>\$95,062.50</b>							4.5 month(s)
Div. 80	<b>8</b>	<b>Construction Managers Fee - Art 6.4 Site supplies, trailers, furniture, cameras, radios, copiers, vehicles, phone, travel, computers, postage, home office staff</b>	<b>\$33,310.39</b>							4.5 month(s)
91-120	<b>9</b>	<b>Contractor Fee</b>	<b>\$96,328.31</b>							Construction Managers Fee - Art 6 O & P - % of Article 8 Cost of the work Items 1-6
91-105	<b>10</b>	<b>Contingency</b>	<b>\$60,205.19</b>							Cost of the work-Owners Contingency
<b>91-145</b>		<b>Pre-Construction Payment</b>	<b>\$29,780.21</b>							Pre-Construction Services
<b>Total Construction Fee based on Contract (Includes Items 7, 8, 9 )</b>			<b>\$224,701.20</b>							
<b>Precon+Fee+GC's+Bonds+Insurance (items 3,4,5,6,6a,7,8,9)</b>			<b>\$490,876.92</b>							
<b>TOTAL GMP</b>			<b>\$1,518,790.48</b>							





# ASSUMPTIONS & CLARIFICATIONS

PROJECT NAME:	SL-04 FIS & BUILDING 846 STORM RESILIENCY MODIFICATIONS PACKAGE 2
LEBOLO PROJECT No:	2021-0024
PBIA PROJECT No:	DOA 18-2A SL-04
VERSION:	4.0
PROPOSAL DATE:	Monday, March 21, 2022

FORM LCM-PC-04 | 08/20/2021

PALM BEACH COUNTY DEPARTMENT OF AIRPORTS	
No.	Work Division
	<b>DIVISION 1 - GENERAL</b>
1	The Contract Sum and the amount of each item are based upon the costs of materials and labor as they exist on the date of the contract. Owner and contractor acknowledge that market conditions are being adversely affected by international market conditions, unusually adverse weather conditions and other not reasonably foreseeable events that are not within the reasonable control of the owner or contractor. Accordingly, in the event that costs for any substantive item or element of materials and/or supplies, shall increase after the date of this contract and during the time of performance of same, and such cost increases are due to the above described events that are beyond the control of the Owner and the Contractor, then the Contractor shall be entitled to an equitable adjustment of the Contract Sum to reasonably compensate the Contractor for these increases.
2	Work to be performed Monday to Friday 7AM to 5PM on rooftop work and after hours for interior work.
3	Temporary power and water being available within 50' of project location.
4	All costs shown to be added are direct costs.
5	Cost is based on plans and specifications provided.
6	Assumed that owner will provide a laydown area for dumpsters, bathrooms, storage, etc. close to 846 Building.
7	All Permits and Permit Fees assumed by owner.
8	Secondary Permit Fees assumed as refundables. Allowance included, see Allowance Exhibit E.
9	Impact fees are excluded.
10	Textura Fees are included.
11	No provision included for special inspections.
12	Rental property for storage of materials and equipment is excluded.
13	Parking Fees are excluded.
14	Removal or studies of hazardous materials are excluded.
15	Work or modifications for the Public Address system are excluded
16	BDA system is not included.
17	Alta Survey is not included.
	<b>DIVISION 5 - METALS</b>
1	Steel - Corrections or repairs to existing to remain not included.
	<b>DIVISION 7 - THERMAL &amp; MOISTURE PROTECTION</b>
1	Roofing - Roofing area will be protected during chiller replacement activity and steel installation. LEBOLO will provide a visual inspection of the roof before to start the work. We suggest for PBIA to do a roof report with the warranty holder vendor before mobilization.
2	Roofing - An allowance for patch and repairs after roof work is included.



# ASSUMPTIONS & CLARIFICATIONS

PROJECT NAME:	SL-04 FIS & BUILDING 846 STORM RESILIENCY MODIFICATIONS PACKAGE 2
LEBOLO PROJECT No:	2021-0024
PBIA PROJECT No:	DOA 18-2A SL-04
VERSION:	4.0
PROPOSAL DATE:	Monday, March 21, 2022

FORM LCM-PC-04 | 08/20/2021

PALM BEACH COUNTY DEPARTMENT OF AIRPORTS	
No.	Work Division
<b>DIVISION 9 - FINISHES</b>	
1	Acoustical Ceiling - Additional demo and replace grid and removal and reinstall tiles due to actual removal conditions included as allowance.
2	Painting - Paint over steel structure patch and repairs only after welding areas included. Match color is not possible.
<b>DIVISION 15 - MECHANICAL WORK</b>	
1	HVAC - Filters for existing equipment's required for T&B assumed by owner.
2	HVAC - Excluded motor starters and VFD's other than what is supplied by HVAC vendors shown on Mechanical drawings and in the specifications.
3	HVAC - Duct cleaning is included.
4	HVAC - 12 Month warranty starting at equipment startup included. 5 year parts & labor warranty on new chillers.
5	HVAC - If two (2) 1.5 Ton temporary spot coolers to be included add \$3,000 per week.
6	HVAC - One (1) 100 Ton temporary chiller with hoses included.
7	HVAC - Removal of existing EMS/BAS controls, wiring, conduit and devices other than what is required to tie in new EMS controls is excluded.
8	Fire Protection - Fire Protection to provide labor and material to disconnect an existing 1 1/4" BL because is in conflict with the New Structural Member to be installed. This relocation is up to 10 Ft over. This proposal is also including plugging a total of 6 Hds. in the area of work to prevent any water damage during the installation of the New Structural Member. Once the new Structural member is installed we will come back and re-install the hds (New Sprinkler Hds) in this area. NO Sprinkler relocation is included in this proposal as this could affect the Layout/proper coverage of the space (Area of Work).
<b>DIVISION 16 - ELECTRICAL WORK</b>	
1	Lightning Protection - Any needed repairs to the existing lightning protection system are excluded. UL Recertification included.
2	Low Voltage - Allowance for Antennas service if required is included.
3	Electrical - Switchboard specs are unknown, breakers cost is included as allowance for \$3,000ea.





# ALLOWANCES

PROJECT NAME:	SL-04 FIS & BUILDING 846 STORM RESILIENCY MODIFICATIONS PACKAGE 2
LEBOLO PROJECT No:	2021-0024
PBIA PROJECT No:	DOA 18-2A SL-04
VERSION:	4.0
PROPOSAL DATE:	Monday, March 21, 2022

FORM LCM-PC-05 | 08/20/2021

PALM BEACH COUNTY DEPARTMENT OF AIRPORTS		
No.	Description	Cost \$
	<b>DIVISION 1 - GENERAL</b>	
1	Secondary Permit Fees (Subcontractors)	\$0.00
2	Subcontractor's Bond Cost over \$100,000	\$19,624.11
	<b>DIVISION 7 - THERMAL &amp; MOISTURE PROTECTION</b>	
1	Roofing - Patch & repairs	\$3,000.00
	<b>DIVISION 9 - FINISHES</b>	
1	Acoustical Ceiling - Additional repairs due to actual removal conditions	\$5,000.00
	<b>DIVISION 16 - ELECTRICAL WORK</b>	
1	Low Voltage - Antennas service if required - add	\$2,500.00
2	Electrical - Disconnects	\$6,000.00

SECTION B

# **Construction Phase Management Fee**

## **General Conditions**







# CONSTRUCTION PHASE MANAGEMENT FEE

PROJECT NAME:	SL-04 FIS & BUILDING 846 STORM RESILIENCY MODIFICATIONS PACKAGE 2		
LEBOLO PROJECT No:	2021-0024		
PBIA PROJECT No:	DOA 18-2A SL-04		
VERSION:	4.0		
PROPOSAL DATE:	Monday, March 21, 2022		

Project Estimate Duration - On Site	140.0	days
	20.0	week(s)
	4.5	month(s)

FORM LCM-PC-43 | 08/20/2021

GENERAL CONDITIONS DIV.80									
LEBOLO COST CODE	SPEC. COST CODE	PERSONNEL	Qty	Unit	Labor Unit Cost	Labor Total	Material Unit Cost	Material Total	Total
80-120		FIELD SUPERVISION							\$95,063
		Superintendent	4.50	mith	\$13,500	\$60,750		\$0	\$60,750
80-215		PROJECT MANAGEMENT							\$34,313
		Senior Project Manager	0.23	mith	\$14,500	\$3,263		\$0	\$3,263
80-220		Project Manager	1.80	mith	\$13,500	\$24,300		\$0	\$24,300
80-285		Project Coordinator	0.90	mith	\$7,500	\$6,750		\$0	\$6,750
GENERAL CONDITIONS TOTAL						\$95,062.50		\$0.00	\$95,062.50
									OK



# GENERAL CONDITIONS

PROJECT NAME:	SL-04 FIS & BUILDING 846 STORM RESILIENCY MODIFICATIONS PACKAGE 2		
LEBOLO PROJECT No:	2021-0024		
PBJA PROJECT No:	DOA 18-2A SL-04		
VERSION:	4.0		
PROPOSAL DATE:	Monday, March 21, 2022		

Project Estimate Duration - On Site	140.0	days
	20.0	week(s)
	4.5	month(s)

FORM LCM-PC-03 | 08/20/2021

GENERAL CONDITIONS DIV.80										
LEBOLO COST CODE	SPEC. COST CODE	TEMPORARY TRAILER & STORAGE	Qty	Unit	Labor Unit Cost	Labor Total	Material Unit Cost	Material Total	Total	
80-410		Trailer/Office Buildout & Setup	1.00	ea			\$0	\$2,200	\$2,200	\$17,050
80-405		Office Trailer and Related Expenses	4.50	mtl			\$0	\$3,300	\$14,850	
80-441		Ground Level Storage Container Setup	2.00	ea			\$0	\$335	\$670	
80-440		Ground Level Storage Container	2.25	mtl			\$0	\$198	\$445	
LEBOLO COST CODE	SPEC. COST CODE	SAFETY	Qty	Unit	Labor Unit Cost	Labor Total	Material Unit Cost	Material Total	Total	
80-540		Safety/Protection	1.00	ls			\$0	\$11,720.00	\$11,720	\$11,720
LEBOLO COST CODE	SPEC. COST CODE	PROJECT CLOSEOUT	Qty	Unit	Labor Unit Cost	Labor Total	Material Unit Cost	Material Total	Total	
80-270		Close Out Administrator	1.00	ls			\$0	\$500	\$500	\$500
LEBOLO COST CODE	SPEC. COST CODE	LISS	Qty	Unit	Labor Unit Cost	Labor Total	Material Unit Cost	Material Total	Total	
80-045		LISS - Lebolo Integrated Software Solutions	4.50	month		\$650	\$2,925	\$0	\$2,925	\$2,925
GENERAL CONDITIONS TOTAL						\$2,925.00		\$30,385.39	\$33,310.39	OK



SECTION C

# Reimbursable General Conditions







# GENERAL REQUIREMENTS

PROJECT NAME: SL-04 FIS & BUILDING 846 STORM  
RESILIENCY MODIFICATIONS PACKAGE

2

LEBOLO PROJECT No: 2021-0024

PBIA PROJECT No: DOA 18-2A SL-04

VERSION: 4.0

PROPOSAL DATE: Monday, March 21, 2022

Project Estimate Duration - On Site 140.0 days  
20.0 week(s)  
4.5 month(s)

FORM LCM-PC-02 | 03/20/2021

## GENERAL REQUIREMENTS DIV.17

LEBOLO COST CODE	SPEC. COST CODE	SAFETY	Qty	Unit	Labor Unit Cost	Labor Total	Material Unit Cost	Material Total	Total
17-110		Safety Inspections/Misc.	4.50	mth		\$0	\$950	\$4,275	\$4,275
CLEANING									
17-205		Clean-up	80.00	hr	\$55	\$4,400		\$0	\$4,400
17-210		Final Cleaning	1.00	ls	\$1,750	\$1,750		\$0	\$1,750
17-220		Dumpsters	10.0	ea	\$1,500	\$15,000		\$0	\$15,000
17-225		Temporary Toilets	4.50	2*mth	\$100	\$450	\$250	\$2,250	\$2,700
TEMPORARY SERVICES									
17-305		Temporary Fence	1.00	ls	\$2,000	\$2,000		\$0	\$2,000
17-310		Temporary Power	1.00	ls		\$0	\$5,000	\$5,000	\$5,000
TEMPORARY OFFICE									
17-665		Plans & Documents	4.50	set*pg*mth		\$0	\$40	\$180	\$180
OTHER GENERAL REQUIREMENTS									
17-950		Textura	1.00	ls	\$9,000	\$9,000		\$0	\$9,000
GENERAL REQUIREMENTS TOTAL									\$44,305.40
									OK

SECTION D

# Minority Participation Report







# MINORITY PARTICIPATION REPORT

## PALM BEACH COUNTY DEPARTMENT OF AIRPORTS

DOA 18-13 CM@RISK SERVICES for MISCELLANEOUS  
IMPROVEMENTS PROJECTS on a CONTINUING CONTRACT BASIS

PBI Project No.	LEBOLO Project No.	Project Name	GMP BASE BID	DIRECT COST	EBO CERTIFICATION	SBE	MBE	WBE	OTHER MINORITY	TOTAL MINORITY PARTICIPATION	%	Status
SL-04	2020-0024	<u>Storm Resiliency Package Phase 2</u>	\$ 1,518,790.48	\$ 967,708.37								
		<b>SUBCONTRACTORS</b>										
SL-04	2020-0024	All American Ceilings		\$ 31,988.04	No	\$ -	\$ -	\$ -	\$ -	\$ -	0%	
SL-04	2020-0024	Van Linda Iron		\$ 210,788.50	Yes	\$ 210,789	\$ -	\$ -	\$ -	\$ 210,789	22%	
SL-04	2020-0024	Roofing Package LEBOLO Allowance		\$ 3,000.00	No	\$ -	\$ -	\$ -	\$ -	\$ -	0%	
SL-04	2020-0024	I.O. Constructions		\$ 39,750.00	Yes	\$ 39,750	\$ -	\$ -	\$ -	\$ 39,750	4%	
SL-04	2020-0024	Johnsons Controls		\$ 3,685.83	No	\$ -	\$ -	\$ -	\$ -	\$ -	0%	
SL-04	2020-0024	Quantum Mechanical		\$ 637,296.00	Yes	\$ 637,296	\$ -	\$ -	\$ -	\$ 637,296	66%	
SL-04	2020-0024	Protect Video		\$ 33,600.00	Yes	\$ 33,600	\$ -	\$ -	\$ -	\$ 33,600	3%	
SL-04	2020-0024	Bonded Lightning		\$ 5,100.00	No	\$ -	\$ -	\$ -	\$ -	\$ -	0%	
SL-04	2020-0024	Low Voltage Package LEBOLO Allowance		\$ 2,500.00	No	\$ -	\$ -	\$ -	\$ -	\$ -	0%	
<b>TOTAL</b>			<b>\$ 1,518,790.48</b>	<b>\$ 967,708.37</b>		<b>\$ 921,435</b>	<b>\$ -</b>	<b>\$ -</b>	<b>\$ -</b>	<b>\$ 921,435</b>	<b>95%</b>	
						<b>95.22%</b>	<b>0.00%</b>	<b>0.00%</b>	<b>0.00%</b>		<b>95.22%</b>	<b>*Based on Direct Cost</b>
						<b>60.67%</b>	<b>0.00%</b>	<b>0.00%</b>	<b>0.00%</b>		<b>60.67%</b>	<b>*Based on Total Cost</b>
						<b>SBE</b>	<b>MBE</b>	<b>WBE</b>	<b>OTHER MINORITY</b>			

SECTION E

# Subcontractor Bidding Status Report





## Project:2020-0024 PBI Storm Resiliency Modifications Package 2 - Invited - List All

TOTAL INVITED	216
PROPOSED	13
DECLINED	203

Group By	Company Name	Status	Certification Abbreviation	Last Activity On	Notes
02020 - Selective Demolition	Bader Demolition	Declined			
	Cushing Demolition	Declined			
	Demcon Group	Declined	NONE, N/A Cert		
	I.Q. Constructions, Inc	Proposed	SBE, M/WBE, N/A Cert	02/21/2022 16:14	01-05-2022 11:32 AM Juna Hagaman said: Bidding. 02-10-2022 2:57 PM Sebastian Fonnegra said: final request sent
	J Sterling Services	Declined			
	Midway Corp.	Declined			
	N & P Construction and Development	Proposed	MWBE	02/07/2022 11:01	01-12-2022 7:47 AM Sub Tony Piedra said: Good morning! Thank you for the invitation. I'll be at the site visit. My name is Tony Piedra (561) 644-2443. Thank you.
	North Star Contractors	Declined	SWBE, ESBE, NRCA		01-05-2022 11:21 AM Juna Hagaman said: Not Bidding
	Others Construction	Declined			
	Pronto Construction Developers	Declined	SBE, MBE, MBE-DBE, DBE/MBE, DBE, DBE-MBE, CBE, ACI		
	Rapid Removal	Declined	SBE		02-10-2022 2:55 PM Sebastian Fonnegra said: Resent for demo, 02-25-2022 9:13 AM Sebastian Fonnegra said: No answer - Not interested
	The BG Group	Declined	WBE, N/A Cert	01/11/2022 13:40	
	Wildcat Demolition	Declined	SBE		
05005 - Structural Steel Package					
	A Ultimate Fabrication & Welding Services	Declined	NONE, AISC		01-04-2022 11:06 AM Juna Hagaman said: Did receive email and will review., 02-25-2022 9:13 AM Sebastian Fonnegra said: No answer - Not interested
	AAA Steel Fabricators Inc	Declined			01-04-2022 11:08 AM Juna Hagaman said: Will review., 02-25-2022 9:13 AM Sebastian Fonnegra said: No answer - Not interested
					01-04-2022 11:09 AM Juna Hagaman said: Accentwelding@gmail.com, 01-04-2022 11:11 AM Juna Hagaman said: Accentwelding@gmail.com Added and resent, 02-25-2022 9:13 AM Sebastian Fonnegra said: No answer - Not interested
	Accent WElding	Declined			
	ADF International Inc.	Declined	NONE, AISC FAB	01/05/2022 09:34	02-25-2022 9:13 AM Sebastian Fonnegra said: No answer - Not interested
					01-04-2022 11:15 AM Juna Hagaman said: Will review and will visit site visit if decide to bid., 02-25-2022 9:13 AM Sebastian Fonnegra said: No answer - Not interested
	America CMS	Declined			
	Arriaga Steel	Declined			01-04-2022 11:17 AM Juna Hagaman said: VM Full, 02-25-2022 9:13 AM Sebastian Fonnegra said: No answer - Not interested
					01-04-2022 11:19 AM Juna Hagaman said: VM, 02-25-2022 9:14 AM Sebastian Fonnegra said: No answer - Not interested
	Associated Steel & Aluminum	Declined			01-04-2022 11:20 AM Juna Hagaman said: Not Bidding
	Associated Steel & Aluminum Ltd Int	Declined			01-04-2022 11:21 AM Juna Hagaman said: Not Bidding
	Bandy Universal Inc	Declined			
	Buck Steel	Declined			01-04-2022 11:23 AM Juna Hagaman said: Not Bidding Not profitable for them.
					01-04-2022 11:25 AM Juna Hagaman said: Review, 02-25-2022 9:14 AM Sebastian Fonnegra said: No answer - Not interested
	Canuke Enterprises	Declined			01-04-2022 11:26 AM Juna Hagaman said: VM, 02-25-2022 9:14 AM Sebastian Fonnegra said: No answer - Not interested
	Castle Welding Inc dba J & R Welding	Declined			01-04-2022 11:28 AM Juna Hagaman said: Review, 02-25-2022 9:14 AM Sebastian Fonnegra said: No answer - Not interested
	CBR Steel Fabricators & Erectors	Declined			01-04-2022 11:29 AM Juna Hagaman said: No Airport projects. Not Bidding
					01-04-2022 11:33 AM Juna Hagaman said: He will respond to email, 02-25-2022 9:14 AM Sebastian Fonnegra said: No answer - Not interested
	Coastal Welding & Fabrications	Declined			01-04-2022 11:35 AM Juna Hagaman said: Will remind Don., 02-25-2022 9:15 AM Sebastian Fonnegra said: No answer - Not interested
	Commercial Metal Buildings (CMB)	Declined			
	Composite Systems Inc.	Declined			
					01-04-2022 11:36 AM Juna Hagaman said: Call after Jan 4th., 01-04-2022 11:36 AM Juna Hagaman said: Call after Jan 4th. Return from vacation., 02-25-2022 9:15 AM Sebastian Fonnegra said: No answer - Not interested
	Custom Welding Diversified, Inc	Declined			01-04-2022 11:38 AM Juna Hagaman said: VM, 02-25-2022 9:15 AM Sebastian Fonnegra said: No answer - Not interested
	D & D Welding and Fabrication, LLC	Declined			01-04-2022 11:39 AM Juna Hagaman said: Not Bidding
	D W RECREATION SERVICES INC	Declined	DBE		01-04-2022 11:40 AM Juna Hagaman said: VM, 02-25-2022 9:15 AM Sebastian Fonnegra said: No answer - Not interested
	DBK Construction	Declined			
	Dosdourian Enterprises Inc	Declined			
	Durabuilt Construction LLC	Declined			01-04-2022 11:43 AM Juna Hagaman said: Steel pilings
					01-04-2022 11:44 AM Juna Hagaman said: Review, 02-25-2022 9:16 AM Sebastian Fonnegra said: No answer - Not interested
	Dynamic Contractor Services LLC	Declined			01-04-2022 11:45 AM Juna Hagaman said: Review, 02-25-2022 9:16 AM Sebastian Fonnegra said: No answer - Not interested
	Eagle Metal Products Inc.	Declined		01/20/2022 14:53	01-04-2022 11:47 AM Juna Hagaman said: Review, 02-25-2022 9:16 AM Sebastian Fonnegra said: No answer - Not interested
	East Coast Metal Structures	Declined	WBE/MBE, ABC, AGC, AISC	02/07/2022 10:16	01-04-2022 11:49 AM Juna Hagaman said: Copied info., 02-25-2022 9:16 AM Sebastian Fonnegra said: No answer - Not interested
	Evans Roofing	Declined			
					01-04-2022 11:54 AM Juna Hagaman said: He is interested. Will review today., 02-25-2022 9:16 AM Sebastian Fonnegra said: No answer - Not interested
	Florida Steel Buildings System	Declined			01-04-2022 11:55 AM Juna Hagaman said: Closed after 48 Years
	Florida Welding Fabricators & Erectors	Declined			01-04-2022 11:56 AM Juna Hagaman said: Not Bidding
	Hofmann Investments	Declined			
					01-04-2022 11:57 AM Juna Hagaman said: Incorrect phone number. Private #!, 02-25-2022 9:16 AM Sebastian Fonnegra said: No answer - Not interested
	Hollywood Iron Works	Declined			01-04-2022 11:57 AM Juna Hagaman said: Duplicate, 02-25-2022 9:16 AM Sebastian Fonnegra said: No answer - Not interested
	Hollywood Ironworks	Declined			
	Jacob Erecting & Construction	Declined			01-05-2022 8:44 AM Juna Hagaman said: Call cannot be completed at this time.
	Jupiter Welding	Declined	N/A, N/A Cert		01-05-2022 8:45 AM Juna Hagaman said: VM, 02-25-2022 9:17 AM Sebastian Fonnegra said: No answer - Not interested
					01-05-2022 8:46 AM Juna Hagaman said: Wireless caller is unavailable., 02-25-2022 9:17 AM Sebastian Fonnegra said: No answer - Not interested
	Limitless Contractors Corp	Declined			01-05-2022 8:53 AM Juna Hagaman said: Anthony will review., 02-25-2022 9:17 AM Sebastian Fonnegra said: No answer - Not interested
	Metal Supply	Declined	NONE, N/A Cert		
					01-05-2022 8:53 AM Juna Hagaman said: Disconnected, 02-25-2022 9:17 AM Sebastian Fonnegra said: No answer - Not interested
	Metal Tech Design Inc	Declined			01-05-2022 8:59 AM Juna Hagaman said: Will attend site visit., 02-25-2022 9:17 AM Sebastian Fonnegra said: No answer - Not interested
	Palm Beach Iron Works	Declined	SBE	02/07/2022 11:41	
					01-05-2022 9:01 AM Juna Hagaman said: She will remind them of site visit., 02-25-2022 9:17 AM Sebastian Fonnegra said: No answer - Not interested
	Sembco, Inc.	Declined			01-05-2022 9:03 AM Juna Hagaman said: She will remind them to review., 01-05-2022 9:34 AM Juna Hagaman said: She will remind them to review. Added and resent: estimating@skylinesteel.com, 02-25-2022 9:17 AM Sebastian Fonnegra said: No answer - Not interested
	Skyline Steel Inc	Declined		01/05/2022 10:05	01-05-2022 9:08 AM Juna Hagaman said: VM, 02-25-2022 9:17 AM Sebastian Fonnegra said: No answer - Not interested
	Southern Custom Iron & Art	Declined	SBE		01-05-2022 9:11 AM Juna Hagaman said: VM, 02-25-2022 9:18 AM Sebastian Fonnegra said: No answer - Not interested
	Sparks Metalworks	Declined		01/10/2022 10:34	



## Project:2020-0024 PBI Storm Resiliency Modifications Package 2 - Invited - List All

TOTAL INVITED	216
PROPOSED	13
DECLINED	203

Group By	Company Name	Status	Certification Abbreviation	Last Activity On	Notes
	Steel Fabricators	Declined	N/A, ABC, AGC, AISC ERE, AISC FAB		01-05-2022 9:13 AM Juna Hagaman said: Not Bidding
	Steel Fabricators and Welding, Inc	Declined			01-05-2022 9:14 AM Juna Hagaman said: Not Bidding
	SteelCast Builders	Declined			01-05-2022 9:15 AM Juna Hagaman said: Fax number, 02-25-2022 9:18 AM Sebastian Fonnegra said: No answer - Not interested
	STERLING STEEL FABRICATIONS, INC	Declined	SBE, DBE/MBE		01-05-2022 9:16 AM Juna Hagaman said: Gates, Railings, stairs No Structural work. Not Bidding, 02-25-2022 9:18 AM Sebastian Fonnegra said: No answer - Not interested
	Structural And Metal Services LLC	Declined		01/05/2022 15:35	01-05-2022 9:23 AM Juna Hagaman said: Will attend site visit., 01-05-2022 9:31 AM Juna Hagaman said: Will attend site visit. Added and resent : structuralmetal@outlook.com, 02-25-2022 9:18 AM Sebastian Fonnegra said: No answer - Not interested
	Suncor	Declined	NONE, AISC FAB		01-05-2022 9:38 AM Juna Hagaman said: Scott will look at it., 02-25-2022 9:19 AM Sebastian Fonnegra said: No answer - Not interested
	Tan Construction Services	Declined			01-05-2022 9:41 AM Juna Hagaman said: Wrong number as of 3 years ago., 02-25-2022 9:18 AM Sebastian Fonnegra said: No answer - Not interested
	Treasure Coast Ornamental Iron	Declined			01-05-2022 9:43 AM Juna Hagaman said: VM, 02-25-2022 9:18 AM Sebastian Fonnegra said: No answer - Not interested
	Tru-Steel Corp.	Declined			01-05-2022 9:45 AM Juna Hagaman said: Took our phone number., 02-25-2022 9:19 AM Sebastian Fonnegra said: No answer - Not interested
	TWS Fabricators	Proposed	SBE	02/10/2022 08:56	01-05-2022 9:40 AM Juna Hagaman said: She will remind Bill.
	Valencia Welding	Declined			01-05-2022 9:46 AM Juna Hagaman said: Review, 02-25-2022 9:19 AM Sebastian Fonnegra said: No answer - Not interested
	Van Linda Iron Works, Inc.	Proposed	SBE, AISC FAB	02/10/2022 07:40	
	VM Iron Works & Stuctural Steel Co	Declined		02/10/2022 13:49	01-05-2022 9:48 AM Juna Hagaman said: On their list to bid., 02-25-2022 9:19 AM Sebastian Fonnegra said: No answer - Not interested
	Walker Design & Construction	Declined	SBE, ABC	01/04/2022 21:14	02-25-2022 9:19 AM Sebastian Fonnegra said: No answer - Not interested
	Wallaby's Fabrications LLC	Declined			01-05-2022 9:50 AM Juna Hagaman said: Took info., 02-25-2022 9:19 AM Sebastian Fonnegra said: No answer - Not interested
	Wentworth Construction	Declined			01-05-2022 9:51 AM Juna Hagaman said: Out of service., 02-25-2022 9:19 AM Sebastian Fonnegra said: No answer - Not interested
	West Palm Machining & Welding, Inc	Declined		02/07/2022 11:45	01-05-2022 9:54 AM Juna Hagaman said: He will discuss with partners., 02-25-2022 9:19 AM Sebastian Fonnegra said: No answer - Not interested
	West Point Industries	Declined			01-05-2022 9:55 AM Juna Hagaman said: Out of service, 02-25-2022 9:19 AM Sebastian Fonnegra said: No answer - Not interested
	WG Fabricators, LLC	Declined			01-05-2022 9:56 AM Juna Hagaman said: Out of service, 02-25-2022 9:19 AM Sebastian Fonnegra said: No answer - Not interested
	YATS Construction	Declined			01-05-2022 9:58 AM Juna Hagaman said: Will attend site visit. Sending name of rep to our email., 02-25-2022 9:20 AM Sebastian Fonnegra said: No answer - Not interested
	Yukon Construction, Inc.	Declined			01-05-2022 10:04 AM Juna Hagaman said: No VM, 01-05-2022 11:07 AM Juna Hagaman said: Shell contractor
09105 - Drywall & Framing Package					
	ACA CONTRACTORS, INC.	Declined	MWBE, DBE		01-05-2022 10:10 AM Juna Hagaman said: VM, 02-25-2022 9:20 AM Sebastian Fonnegra said: No answer - Not interested
	Acousti Engineering Company of Flo	Declined	N/A, N/A Cert	01/06/2022 08:57	01-05-2022 10:34 AM Juna Hagaman said: Bidding and will remind., 01-05-2022 10:34 AM Juna Hagaman said: Bidding and will remind estimator of site visit., 02-25-2022 9:20 AM Sebastian Fonnegra said: No answer - Not interested
	Alen Construction Group	Declined	SBE, SBE-E, FED SBA 8A, DBE/MBE, DBE, DBE-MBE, CBE, ABC, ACI, AGC, SNAACNA, NAWIC, CSI, ASPE		01-05-2022 10:38 AM Juna Hagaman said: VM for Angelina, 02-25-2022 9:20 AM Sebastian Fonnegra said: No answer - Not interested
	ALLENMICHE' DEVELOPMENT & CO	Declined	DBE/MBE		01-05-2022 10:43 AM Juna Hagaman said: VM, 02-25-2022 9:21 AM Sebastian Fonnegra said: No answer - Not interested
	Applegate Interiors	Declined	SBE, MWBE		01-05-2022 10:46 AM Juna Hagaman said: She suggested an email be sent to remind him., 02-25-2022 9:23 AM Sebastian Fonnegra said: No answer - Not interested
	Aron & Associates	Declined			01-05-2022 10:48 AM Juna Hagaman said: Not Bidding
	Atlantic Interior Services	Declined	SBE, SBE-E, N/A Cert	01/03/2022 14:55	01-05-2022 10:51 AM Juna Hagaman said: Not Bidding
	Best Build	Declined	SBE, DBE/MBE		01-05-2022 10:52 AM Juna Hagaman said: VM, 02-25-2022 9:23 AM Sebastian Fonnegra said: No answer - Not interested
	CI Painting	Declined			02-25-2022 9:21 AM Sebastian Fonnegra said: No answer - Not interested
	CREATIVE CONTRACTING GROUP	Declined	MWBE		01-05-2022 10:58 AM Juna Hagaman said: Suggested a reminder email., 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	CRITICAL PATH CONSTRUCTION (PA	Declined	MWBE, DBE/MBE		01-05-2022 11:01 AM Juna Hagaman said: Will review., 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	FMA CONSTRUCTION	Declined	MBE, DBE/MBE, AWCI		02-25-2022 9:21 AM Sebastian Fonnegra said: No answer - Not interested
	GAST CONSTRUCTION GROUP, INC.	Declined	SBE		01-05-2022 11:09 AM Juna Hagaman said: No VM, 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	I.Q. Constructions, Inc	Proposed	SBE, M/WBE, N/A Cert	02/21/2022 16:14	01-05-2022 11:32 AM Juna Hagaman said: Bidding, 02-10-2022 2:57 PM Sebastian Fonnegra said: Final request sent
	Interior Textures	Declined			01-05-2022 11:34 AM Juna Hagaman said: VM, 02-25-2022 9:21 AM Sebastian Fonnegra said: No answer - Not interested
	MLS CONSTRUCTION, LLC.	Declined	MWBE		01-05-2022 11:21 AM Juna Hagaman said: VM, 02-25-2022 9:25 AM Sebastian Fonnegra said: No answer - Not interested
	North Star Contractors	Declined	SWBE, ESBE, NRCA		01-05-2022 11:21 AM Juna Hagaman said: Not Bidding
	Precision Interiors, Inc.	Declined	NONE, N/A Cert		01-05-2022 11:36 AM Juna Hagaman said: VM, 02-25-2022 9:21 AM Sebastian Fonnegra said: No answer - Not interested
	Reynolds Construction Services	Declined	SBE, PDCA		01-05-2022 11:37 AM Juna Hagaman said: VM, 02-25-2022 9:21 AM Sebastian Fonnegra said: No answer - Not interested
	S35 CONSTRUCTION INC	Declined	DBE/MBE		01-05-2022 11:26 AM Juna Hagaman said: General Contractor
	SAJO MANAGEMENT GROUP LLC DB	Declined	DBE		01-04-2022 10:20 AM Juna Hagaman said: Owner will review tomorrow and respond to email., 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
	Scott Murphy Plastering Inc.	Declined			01-05-2022 11:38 AM Juna Hagaman said: Out of service, 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
	Walker Gerrits Construction	Declined	DBE/MBE		01-05-2022 11:30 AM Juna Hagaman said: VM, 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
09205 - Acoustical Ceiling Package					
	A Beautiful Ceiling	Declined			01-05-2022 10:06 AM Juna Hagaman said: Not Bidding
	A Ceiling Contractors, Inc.	Declined			01-05-2022 10:07 AM Juna Hagaman said: VM, 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
	ABURI LLC	Declined			01-05-2022 10:08 AM Juna Hagaman said: Not Bidding
	ACA CONTRACTORS, INC.	Declined	MWBE, DBE		01-05-2022 10:10 AM Juna Hagaman said: VM, 02-25-2022 9:20 AM Sebastian Fonnegra said: No answer - Not interested
	ACCEL Construction	Declined	DBE/MBE		01-05-2022 10:28 AM Juna Hagaman said: VM, 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
	Acousti Engineering Company of Flo	Declined	N/A, N/A Cert	01/06/2022 08:57	01-05-2022 10:34 AM Juna Hagaman said: Bidding and will remind., 01-05-2022 10:34 AM Juna Hagaman said: Bidding and will remind estimator of site visit., 02-25-2022 9:20 AM Sebastian Fonnegra said: No answer - Not interested



## Project:2020-0024 PBI Storm Resiliency Modifications Package 2 - Invited - List All

TOTAL INVITED	216
PROPOSED	13
DECLINED	203

Group By	Company Name	Status	Certification Abbreviation	Last Activity On	Notes
	ACP CONSTRUCTION INC	Declined	DBE		01-05-2022 10:35 AM Juna Hagaman said: Silence on phone, 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
	Alen Construction Group	Declined	SBE, SBE-E, FED SBA BA, DBE/MBE, DBE, DBE-MBE, CBE, ABC, ACI, AGC, SMACNA, NAWIC, CSI, ASPE		01-05-2022 10:38 AM Juna Hagaman said: VM for Angelina, 02-25-2022 9:20 AM Sebastian Fonnegra said: No answer - Not interested
	All American Ceilings Inc	Proposed	ABE, ABC		01-05-2022 10:41 AM Juna Hagaman said: Bidding, 02-10-2022 2:59 PM
	ALLENMICHE' DEVELOPMENT & CO	Declined	DBE/MBE		01-05-2022 10:43 AM Juna Hagaman said: VM, 02-25-2022 9:21 AM Sebastian Fonnegra said: No answer - Not interested
	American Construction Services	Declined	N/A, ABC		01-05-2022 10:45 AM Juna Hagaman said: She will remind Wagner, 02-25-2022 9:23 AM Sebastian Fonnegra said: No answer - Not interested
	Applegate Interiors	Declined	SBE, MWBE		01-05-2022 10:46 AM Juna Hagaman said: She suggested an email be sent to remind him, 02-25-2022 9:23 AM Sebastian Fonnegra said: No answer - Not interested
	Aron & Associates	Declined			01-05-2022 10:48 AM Juna Hagaman said: Not Bidding
	Assured Contracting LLC	Declined			01-05-2022 10:49 AM Juna Hagaman said: Impact Windows and doors, 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	Atlantic Interior Services	Declined	SBE, SBE-E, N/A Cert	01/03/2022 14:55	01-05-2022 10:51 AM Juna Hagaman said: Not Bidding
	Best Build	Declined	SBE, DBE/MBE		01-05-2022 10:52 AM Juna Hagaman said: VM, 02-25-2022 9:23 AM Sebastian Fonnegra said: No answer - Not interested
	C. SQUARE DEVELOPMENT CO.	Declined	MWBE		01-05-2022 10:53 AM Juna Hagaman said: VM, 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	CCGC, INC.	Declined	MWBE		01-05-2022 10:55 AM Juna Hagaman said: VM, 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	CONTRACTORS SUPPORT SERVICES	Declined	MWBE		01-05-2022 10:56 AM Juna Hagaman said: VM, 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	CREATIVE CONTRACTING GROUP	Declined	MWBE		01-05-2022 10:58 AM Juna Hagaman said: Suggested a reminder email, 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	CRITICAL PATH CONSTRUCTION (PA	Declined	MWBE, DBE/MBE		01-05-2022 11:01 AM Juna Hagaman said: Will review, 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	DORSAINVIL CONSTRUCTION LLC (P	Declined	DBE/MBE		01-05-2022 11:03 AM Juna Hagaman said: VM, 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	FMA CONSTRUCTION	Declined	MBE, DBE/MBE, AWCI		02-25-2022 9:21 AM Sebastian Fonnegra said: No answer - Not interested
	GAST CONSTRUCTION GROUP, INC.	Declined	SBE		01-05-2022 11:09 AM Juna Hagaman said: No VM, 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	JAX CONSTRUCTION & DEVELOPME	Declined	DBE/MBE		01-05-2022 11:10 AM Juna Hagaman said: VM Full, 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	JJI CONSTRUCTION CORP	Declined	DBE/MBE		01-05-2022 11:11 AM Juna Hagaman said: VM Full No accepto mensaje, 01-05-2022 11:18 AM Juna Hagaman said: VM Full No accepto mensaje, 02-25-2022 9:25 AM Sebastian Fonnegra said: No answer - Not interested
	Martin Acoustic, LLC	Declined		01/18/2022 13:20	01-05-2022 11:18 AM Juna Hagaman said: Bidding, 02-25-2022 9:25 AM Sebastian Fonnegra said: No answer - Not interested
	MLS CONSTRUCTION, LLC	Declined	MWBE		01-05-2022 11:21 AM Juna Hagaman said: VM, 02-25-2022 9:25 AM Sebastian Fonnegra said: No answer - Not interested
	North Star Contractors	Declined	SWBE, ESBE, NRCA		01-05-2022 11:21 AM Juna Hagaman said: Not Bidding
	R2T, INC	Declined	MWBE		01-05-2022 11:24 AM Juna Hagaman said: Estimator out sick, 02-25-2022 9:25 AM Sebastian Fonnegra said: No answer - Not interested
	S3S CONSTRUCTION INC	Declined	DBE/MBE		01-05-2022 11:26 AM Juna Hagaman said: General Contractor
	SAJO MANAGEMENT GROUP LLC DB	Declined	DBE		01-04-2022 10:20 AM Juna Hagaman said: Owner will review tomorrow and respond to email, 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
	Superior Interior Systems Inc	Declined	NONE, N/A Cert		01-05-2022 11:28 AM Juna Hagaman said: Not Bidding
	TOTAL SOLUTION CONTRACTORS	Declined	SBE		01-05-2022 11:29 AM Juna Hagaman said: Not in service, 02-25-2022 9:25 AM Sebastian Fonnegra said: No answer - Not interested
	Walker Gerrits Construction	Declined	DBE/MBE		01-05-2022 11:30 AM Juna Hagaman said: VM, 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
09505 - Painting Package	A to Z Paint Contracting	Declined	SWBE, SBE		01-05-2022 11:43 AM Juna Hagaman said: Not Bidding
	A1 Paint, Inc of Palm Beach	Declined	SBE, SBE-E, MBE, NAWIC		02-25-2022 9:25 AM Sebastian Fonnegra said: No answer - Not interested
	ACA CONTRACTORS, INC.	Declined	MWBE, DBE		01-05-2022 10:10 AM Juna Hagaman said: VM, 02-25-2022 9:20 AM Sebastian Fonnegra said: No answer - Not interested
	Advanced Painting Contractors	Declined	N/A, N/A Cert	01/03/2022 15:28	02-25-2022 9:26 AM Sebastian Fonnegra said: Not interested
	Advantage Painting LLC	Declined			02-25-2022 9:37 AM Sebastian Fonnegra said: No answer - Not interested
	Alen Construction Group	Declined	SBE, SBE-E, FED SBA BA, DBE/MBE, DBE, DBE-MBE, CBE, ABC, ACI, AGC, SMACNA, NAWIC, CSI, ASPE		01-05-2022 10:38 AM Juna Hagaman said: VM for Angelina, 02-25-2022 9:20 AM Sebastian Fonnegra said: No answer - Not interested
	ALLENMICHE' DEVELOPMENT & CO	Declined	DBE/MBE		01-05-2022 10:43 AM Juna Hagaman said: VM, 02-25-2022 9:21 AM Sebastian Fonnegra said: No answer - Not interested
	Best Build	Declined	SBE, DBE/MBE		01-05-2022 10:52 AM Juna Hagaman said: VM, 02-25-2022 9:23 AM Sebastian Fonnegra said: No answer - Not interested
	Brookley Wallcoverings	Declined	SBE		01-05-2022 11:44 AM Juna Hagaman said: VM, 02-25-2022 9:26 AM Sebastian Fonnegra said: No answer - Not interested
	Campbell Painting, Inc.	Declined	SBE-E, MBE-E		01-05-2022 11:45 AM Juna Hagaman said: Closing the business
	CCGC, INC.	Declined	MWBE		01-05-2022 10:55 AM Juna Hagaman said: VM, 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	CHAMPION PAINTING SPECIALTY SE	Declined	DBE/MBE		01-05-2022 11:47 AM Juna Hagaman said: Gave me options for NYC and Alaska Not for Florida, 02-25-2022 9:26 AM Sebastian Fonnegra said: No answer - Not interested
	Copax LLC	Declined	WOSB, WCOE		01-05-2022 11:50 AM Juna Hagaman said: Will attend site visit, 01-05-2022 11:52 AM Juna Hagaman said: Will attend site visit. Added and resent: bids@copaxpainting.com, 02-25-2022 9:27 AM Sebastian Fonnegra said: No answer - Not interested
	CREATIVE CONTRACTING GROUP	Declined	MWBE		01-05-2022 10:58 AM Juna Hagaman said: Suggested a reminder email, 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	CRITICAL PATH CONSTRUCTION (PA	Declined	MWBE, DBE/MBE		01-05-2022 11:01 AM Juna Hagaman said: Will review, 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	Dynamic Painting	Declined	WMBE, SBE, DBE/MBE		01-05-2022 11:54 AM Juna Hagaman said: VM
	Eagle Painting (J&J Inc)	Declined	MWBE		02-25-2022 9:27 AM Sebastian Fonnegra said: No answer - Not interested
	G P.S. Painting Group	Declined	SBE		01-05-2022 11:55 AM Juna Hagaman said: Suggested an email reminder be sent, 02-25-2022 9:27 AM Sebastian Fonnegra said: No answer - Not interested
	GAST CONSTRUCTION GROUP, INC.	Declined	SBE		01-05-2022 11:57 AM Juna Hagaman said: Review, 02-25-2022 9:27 AM Sebastian Fonnegra said: No answer - Not interested
	Interior Textures	Declined			01-05-2022 11:09 AM Juna Hagaman said: No VM, 02-25-2022 9:24 AM Sebastian Fonnegra said: No answer - Not interested
	MLS CONSTRUCTION, LLC.	Declined	MWBE		01-05-2022 11:34 AM Juna Hagaman said: VM, 02-25-2022 9:21 AM Sebastian Fonnegra said: No answer - Not interested
					01-05-2022 11:21 AM Juna Hagaman said: VM, 02-25-2022 9:25 AM Sebastian Fonnegra said: No answer - Not interested



## Project:2020-0024 PBI Storm Resiliency Modifications Package 2 - Invited - List All

TOTAL INVITED	216
PROPOSED	13
DECLINED	203

Group By	Company Name	Status	Certification Abbreviation	Last Activity On	Notes
	North Star Contractors	Declined	SWBE, ESBE, NRCA		01-05-2022 11:21 AM Juna Hagaman said: Not Bidding
	QUALITY PAINTING & MORE	Declined	HUD SECTION 3		01-05-2022 11:59 AM Juna Hagaman said: Phone went to fax sound., 02-25-2022 9:27 AM Sebastian Fonnegra said: No answer - Not interested
	R2T, INC	Declined	MWBE		01-05-2022 11:24 AM Juna Hagaman said: Estimator out sick., 02-25-2022 9:25 AM Sebastian Fonnegra said: No answer - Not interested
	Reynolds Construction Services	Declined	SBE, PDCA		01-05-2022 11:37 AM Juna Hagaman said: VM, 02-25-2022 9:21 AM Sebastian Fonnegra said: No answer - Not interested
	S3S CONSTRUCTION INC	Declined	DBE/MBE		01-05-2022 11:26 AM Juna Hagaman said: General Contractor
	SAJO MANAGEMENT GROUP LLC DB	Declined	DBE		01-04-2022 10:20 AM Juna Hagaman said: Owner will review tomorrow and respond to email., 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
	Scott Murphy Plastering Inc.	Declined			01-05-2022 11:38 AM Juna Hagaman said: Out of service, 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
	SELECT COATINGS, INC	Declined	SBE, MBE-E, ASC		01-05-2022 12:01 PM Juna Hagaman said: Concrete resurfacing only.
	Sun Art Painting	Declined	SBE		01-05-2022 12:03 PM Juna Hagaman said: Resent email, 02-25-2022 9:28 AM Sebastian Fonnegra said: No answer - Not interested
	Talbot Painting	Declined	SBE		01-05-2022 12:06 PM Juna Hagaman said: Don looked at plans but no decision., 02-25-2022 9:28 AM Sebastian Fonnegra said: No answer - Not interested
	TOTAL SOLUTION CONTRACTORS	Declined	SBE		01-05-2022 11:29 AM Juna Hagaman said: Not in service., 02-25-2022 9:25 AM Sebastian Fonnegra said: No answer - Not interested
	Walker Gerrits Construction	Declined	DBE/MBE		01-05-2022 11:30 AM Juna Hagaman said: VM, 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
13100 - Lightning Protection	All South Lightning Protection	Proposed	NONE, N/A Cert		
	Bonded Lightning Protection	Proposed			
15105 - Fire Protection Package					
	A.B. Fire Equipment	Declined	SBE		01-06-2022 9:41 AM Juna Hagaman said: Resent., 02-25-2022 9:29 AM Sebastian Fonnegra said: No answer - Not interested
	Alliance Automatic Fire Sprinklers	Declined	SMBE, SBE		01-06-2022 9:42 AM Juna Hagaman said: Phone not in service, 02-25-2022 9:29 AM Sebastian Fonnegra said: No answer - Not interested
	American Eagle Fire Protection Inc	Declined			01-06-2022 9:45 AM Juna Hagaman said: Rick will look at plans., 02-25-2022 9:29 AM Sebastian Fonnegra said: No answer - Not interested
	Brigade Fire Protection	Declined			01-06-2022 9:45 AM Juna Hagaman said: Not Bidding
	Caribbean Fire	Declined			01-06-2022 9:51 AM Juna Hagaman said: Added and resent: Michael Vidal mvidal@caribbeanfire.com, 02-25-2022 9:29 AM Sebastian Fonnegra said: No answer - Not interested
	Farmer & Irwin	Declined	N/A, N/A Cert	02/07/2022 10:05	01-04-2022 9:49 AM Juna Hagaman said: No VM, 01-04-2022 12:17 PM Sebastian Fonnegra said: Jeff will be the SR PM on this Project., 02-25-2022 9:29 AM Sebastian Fonnegra said: No answer - Not interested
	Harpers Fire Sprinkler	Declined	SBE, MWBE		01-06-2022 9:53 AM Juna Hagaman said: VM, 01-06-2022 9:55 AM Juna Hagaman said: Frank called and said he would look at plans., 02-25-2022 9:29 AM Sebastian Fonnegra said: No answer - Not interested
	Johnson Controls Fire Protection	Proposed			02-25-2022 9:10 AM Sebastian Fonnegra said: Proposed
	Metro Fire Protection Services, Inc.	Declined			01-06-2022 9:59 AM Juna Hagaman said: VM, 02-25-2022 9:29 AM Sebastian Fonnegra said: No answer - Not interested
	National Fire Protection	Declined			01-06-2022 10:01 AM Juna Hagaman said: Answering service, 02-25-2022 9:29 AM Sebastian Fonnegra said: No answer - Not interested
	SAJO MANAGEMENT GROUP LLC DB	Declined	DBE		01-04-2022 10:20 AM Juna Hagaman said: Owner will review tomorrow and respond to email., 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
	Sprinklermatic	Declined	NONE, ABC		01-06-2022 10:07 AM Juna Hagaman said: Under Review, 02-25-2022 9:29 AM Sebastian Fonnegra said: No answer - Not interested
	Total Life Safety Corporation	Declined			01-06-2022 10:08 AM Juna Hagaman said: Respond to email, 02-25-2022 9:29 AM Sebastian Fonnegra said: No answer - Not interested
	Wiginton Fire Systems	Declined			01-06-2022 10:09 AM Juna Hagaman said: Scott's VM, 02-25-2022 9:29 AM Sebastian Fonnegra said: No answer - Not interested
15205 - HVAC Package					
	Phoenix Air Conditioning, Inc.	Declined			01-04-2022 10:14 AM Juna Hagaman said: She will ask Chris., 02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested
	AC Power & Comfort	Declined	SBE-E, N/A Cert		01-04-2022 9:25 AM Juna Hagaman said: VM, 02-25-2022 9:30 AM Sebastian Fonnegra said: No answer - Not interested
	Air Handlers of the Palm Beaches	Declined	SBE		01-04-2022 8:35 AM Juna Hagaman said: Out of service.
	Air South Mechanical	Declined	NONE, PHCC		01-04-2022 9:28 AM Juna Hagaman said: VM, 02-25-2022 9:30 AM Sebastian Fonnegra said: No answer - Not interested
	All Year Cooling	Declined			01-04-2022 9:27 AM Juna Hagaman said: If they are interested they will respond., 02-25-2022 9:30 AM Sebastian Fonnegra said: No answer - Not interested
	Altman Air Conditioning	Declined		01/05/2022 08:10	01-04-2022 8:37 AM Juna Hagaman said: Will remind estimator., 01-04-2022 10:11 AM Sebastian Fonnegra said: Contacted - Will review drawings, 02-25-2022 9:30 AM Sebastian Fonnegra said: No answer - Not interested
	Aspen	Declined	EBO, ACCA	01/03/2022 14:55	02-25-2022 9:30 AM Sebastian Fonnegra said: No answer - Not interested
	Big Air Mechanical	Declined	SBE	02/21/2022 18:39	01-04-2022 9:33 AM Juna Hagaman said: Will be at site visit., 02-25-2022 9:30 AM Sebastian Fonnegra said: No answer - Not interested
	Bradley Heating & Air Conditioning	Declined	SBE		01-04-2022 9:34 AM Juna Hagaman said: Will review today and respond to email., 02-25-2022 9:30 AM Sebastian Fonnegra said: No answer - Not interested
	Calix Mechanical Group	Declined			01-04-2022 9:36 AM Juna Hagaman said: Not Bidding
	Cedars Electro-Mechanical Inc.	Proposed	WBE, SBE	01/04/2022 14:19	01-04-2022 9:42 AM Juna Hagaman said: Review today.
	Climax Mechanical Corp	Declined	NONE, N/A Cert	01/20/2022 12:22	01-04-2022 9:43 AM Juna Hagaman said: Review, 02-25-2022 9:30 AM Sebastian Fonnegra said: No answer - Not interested
	Commercial Cooling	Declined			01-04-2022 9:44 AM Juna Hagaman said: Not Bidding
	Cool Solutions A/C	Declined			01-04-2022 9:45 AM Juna Hagaman said: VM, 02-25-2022 9:30 AM Sebastian Fonnegra said: No answer - Not interested
	EDS Air Conditioning	Declined			01-04-2022 9:48 AM Juna Hagaman said: VM, 02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested
	Farmer & Irwin	Proposed	N/A, N/A Cert	02/07/2022 10:05	01-04-2022 9:49 AM Juna Hagaman said: No VM, 01-04-2022 12:17 PM Sebastian Fonnegra said: Jeff will be the SR PM on this Project., 02-25-2022 9:29 AM Sebastian Fonnegra said: No answer - Not interested
	Florida Mechanical LLC	Proposed	SBE	02/08/2022 08:38	01-04-2022 9:52 AM Juna Hagaman said: They are interested and will call Sebastian
	Flowmaster	Declined	SBE		01-04-2022 9:54 AM Juna Hagaman said: VM, 02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested
	General Mechanical Corporation	Declined	SCSDB, SBE, NABE, DBE-MBE, N/A Cert		01-04-2022 10:00 AM Juna Hagaman said: Added and resent: David Cannon dcannon@oesgroup.com, 02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested
	H. Lamm Industries	Declined	NONE, ABC	02/07/2022 12:45	01-04-2022 10:03 AM Juna Hagaman said: Jeff is reviewing and will respond to email., 02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested
	HB Hoffman	Declined	MWBE		01-04-2022 10:03 AM Juna Hagaman said: VM, 02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested

## Project:2020-0024 PBI Storm Resiliency Modifications Package 2 - Invited - List All

TOTAL INVITED	216
PROPOSED	13
DECLINED	203

Group By	Company Name	Status	Certification Abbreviation	Last Activity On	Notes
	INTEG MIAMI LLC	Declined	SBE		01-04-2022 10:09 AM Juna Hagaman said: VM, 02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested
	Matrix Air, LLC	Declined			01-04-2022 10:12 AM Juna Hagaman said: VM, 02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested
	Natal Air Conditioning	Declined	SBE, E, ABC		01-04-2022 10:12 AM Juna Hagaman said: It was passed to owner, 02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested
	Precision Air Systems	Declined	SBE		01-04-2022 10:15 AM Juna Hagaman said: She suggested we send a follow-up email, 02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested
	Quantum Mechanical	Proposed	SBE, SBE-E, MWBE, MWBE, MSBE, DBE/MBE, DBE, N/A Cert	02/10/2022 11:35	01-04-2022 10:18 AM Juna Hagaman said: Review 01-04-2022 10:20 AM Juna Hagaman said: Owner will review tomorrow and respond to email, 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
	SAIO MANAGEMENT GROUP LLC DB	Declined	DBE		01-04-2022 10:23 AM Juna Hagaman said: The menu kept sending me back to menu, 02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested
	Sequit Systems Inc.	Declined	SBE, SBE-E, USGBC		01-04-2022 10:25 AM Juna Hagaman said: Rikch, 01-04-2022 10:27 AM Juna Hagaman said: Resent and added: Richard@smithservices.com, 01-11-2022 9:21 PM This contact has unsubscribed from receiving: - communications on this project only - all project communications - all general communications - all prequal communications Contact said: Not interested, 02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested
	Smithco Service	Declined	SBE		01-04-2022 10:25 AM Juna Hagaman said: Rikch, 01-04-2022 10:27 AM Juna Hagaman said: Resent and added: Richard@smithservices.com, 01-11-2022 9:21 PM This contact has unsubscribed from receiving: - communications on this project only - all project communications - all general communications - all prequal communications Contact said: Not interested, 02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested
	Southeast Mechanical	Declined	BEP, ABC	01/04/2022 08:06	02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested
	Southern Mechanical	Declined		01/03/2022 14:52	02-25-2022 9:31 AM Sebastian Fonnegra said: No answer - Not interested
	Stokes Mechanical	Declined	WBE		01-04-2022 10:29 AM Juna Hagaman said: Jana's VM 02-25-2022 9:32 AM Sebastian Fonnegra said: No answer - Not interested
	Sunshine State	Declined	SBE, MWBE		01-04-2022 10:32 AM Juna Hagaman said: Will be at site visit, 02-25-2022 9:32 AM Sebastian Fonnegra said: No answer - Not interested
	The Alrtex Corp	Declined	SBE		01-04-2022 10:34 AM Juna Hagaman said: She will remind them, 02-25-2022 9:32 AM Sebastian Fonnegra said: No answer - Not interested
	The True-Pros	Declined	SBE		01-04-2022 10:36 AM Juna Hagaman said: First day back after Holidays, 02-25-2022 9:32 AM Sebastian Fonnegra said: No answer - Not interested
	Thermal Concepts	Declined	INONE, ABC		01-04-2022 10:39 AM Juna Hagaman said: Mike VM, 02-25-2022 9:32 AM Sebastian Fonnegra said: No answer - Not interested
	TOTAL SYSTEMS, INC.	Declined	MWBE, DBE		01-04-2022 10:40 AM Juna Hagaman said: Phone just rings busy, 02-25-2022 9:32 AM Sebastian Fonnegra said: No answer - Not interested
	Wright Brothers Contracting Service	Declined			01-04-2022 10:53 AM Juna Hagaman said: Resent to: Vishal Singh vsingh@wrightbrothers.com, 02-25-2022 9:32 AM Sebastian Fonnegra said: No answer - Not interested
16005 - Electrical Package					
	Albert Electric	Declined	SBE		01-06-2022 10:23 AM Juna Hagaman said: VM, 02-25-2022 9:32 AM Sebastian Fonnegra said: No answer - Not interested
	All Lake Electrical	Declined	SBE		01-06-2022 10:24 AM Juna Hagaman said: VM, 01-06-2022 10:26 AM Juna Hagaman said: Not Bidding
	Arlington Electric	Declined			01-06-2022 10:28 AM Juna Hagaman said: Not Bidding
	Bosco Electric	Declined			01-06-2022 10:30 AM Juna Hagaman said: Not bidding
	Bradford Electric	Declined	SBE		01-06-2022 10:33 AM Juna Hagaman said: VM, 02-25-2022 9:32 AM Sebastian Fonnegra said: No answer - Not interested
	BROWN & BROWN ELECTRIC INC	Declined	SBE, MWBE, DBE		01-06-2022 10:33 AM Juna Hagaman said: Not in Service
	C.R. DUJIN	Declined	HUD SECTION 3		01-06-2022 10:35 AM Juna Hagaman said: Resent, 02-25-2022 9:32 AM Sebastian Fonnegra said: No answer - Not interested
	Construct Connect	Declined		02/07/2022 11:36	02-25-2022 9:37 AM Sebastian Fonnegra said: No answer - Not interested
	Construction Journal	Declined			02-25-2022 9:37 AM Sebastian Fonnegra said: No answer - Not interested
	Design Electrical	Declined			01-06-2022 10:38 AM Juna Hagaman said: Review, 02-25-2022 9:33 AM Sebastian Fonnegra said: No answer - Not interested
	Electrical Consulting Services	Declined	SBE		01-06-2022 10:40 AM Juna Hagaman said: She will check with Ken, 02-25-2022 9:33 AM Sebastian Fonnegra said: No answer - Not interested
	ELECTRON PLUS OF FLORIDA, LLC	Declined	SBE		01-06-2022 10:42 AM Juna Hagaman said: Not Bidding
	Ellington Electrical Inc	Declined			01-06-2022 10:46 AM Juna Hagaman said: VM, 02-25-2022 9:33 AM Sebastian Fonnegra said: No answer - Not interested
	Everton Electric LLC	Declined			01-06-2022 10:45 AM Juna Hagaman said: VM, 02-25-2022 9:33 AM Sebastian Fonnegra said: No answer - Not interested
	Fine Line Electric, Inc.	Declined	NONE, ABC		01-06-2022 10:47 AM Juna Hagaman said: Not Bidding
	Firecomm Services LLC	Declined	CMBE, IEC		01-06-2022 10:48 AM Juna Hagaman said: Review, 02-25-2022 9:33 AM Sebastian Fonnegra said: No answer - Not interested
	FLORIDA METRO CONSTRUCTION CO	Declined	SBE, DBE/MBE		01-06-2022 10:51 AM Juna Hagaman said: Added and resent. Sommer Russell & russell@floridametro.com, 02-25-2022 9:33 AM Sebastian Fonnegra said: No answer - Not interested
	Gilmore Electric Company	Declined	SBE		01-06-2022 11:04 AM Juna Hagaman said: VM, 02-25-2022 9:33 AM Sebastian Fonnegra said: No answer - Not interested
	Godfrey Electric	Declined	SBE, IEC		01-06-2022 11:07 AM Juna Hagaman said: Tad VM, 02-25-2022 9:33 AM Sebastian Fonnegra said: No answer - Not interested
	Grid-One Electrical Construction	Declined	SBE		01-06-2022 11:08 AM Juna Hagaman said: Not Bidding
	Guthart Electric	Declined	WOSB, IEC		01-06-2022 11:09 AM Juna Hagaman said: VM, 02-25-2022 9:33 AM Sebastian Fonnegra said: No answer - Not interested
	Intercoastal Electric	Declined	NONE, N/A Cert	01/03/2022 15:21	01-06-2022 11:13 AM Juna Hagaman said: VM, 02-25-2022 9:33 AM Sebastian Fonnegra said: No answer - Not interested
	JAG ELECTRICAL ENTERPRISES INC.	Declined	MWBE, DBE		01-06-2022 11:15 AM Juna Hagaman said: Added and resent. Njardonjag@icloud.com, 02-25-2022 9:33 AM Sebastian Fonnegra said: No answer - Not interested
	JMA Electric	Declined	SBE, MBE, DBE/VBE		01-06-2022 11:17 AM Juna Hagaman said: Will respond to email, 02-25-2022 9:34 AM Sebastian Fonnegra said: No answer - Not interested
	Metro Electric	Declined			01-06-2022 11:19 AM Juna Hagaman said: Recep thought they would bid, 02-25-2022 9:34 AM Sebastian Fonnegra said: No answer - Not interested
	Mr. Wireman (Arbor Electrical Service)	Declined	SWBE, SBE, DBE/MBE		01-06-2022 11:21 AM Juna Hagaman said: Resent to Margaret, 02-25-2022 9:34 AM Sebastian Fonnegra said: No answer - Not interested
	OHMS Electrical Corp.	Declined	SBE, MWBE	01/21/2022 10:32	01-06-2022 11:23 AM Juna Hagaman said: Gabriela, 01-06-2022 11:24 AM Juna Hagaman said: Gabriela Coordinator, 02-25-2022 9:34 AM Sebastian Fonnegra said: No answer - Not interested
	Protect Video	Proposed	WOSB, WBE/MBE, WBE-MBE, SBE, IEC		01-06-2022 11:26 AM Juna Hagaman said: VM, 02-25-2022 9:06 AM Sebastian Fonnegra said: Proposed



## Project:2020-0024 PBI Storm Resiliency Modifications Package 2 - Invited - List All

TOTAL INVITED	216
PROPOSED	13
DECLINED	203

Group By	Company Name	Status	Certification Abbreviation	Last Activity On	Notes
	Proton Electric Service Llc	Declined			01-06-2022 11:27 AM Juna Hagaman said: VM, 02-25-2022 9:34 AM Sebastian Fonnegra said: No answer - Not interested
	PVM Electric	Declined	SBE		01-06-2022 11:29 AM Juna Hagaman said: Suggested wew call back tomorrow., 02-25-2022 9:34 AM Sebastian Fonnegra said: No answer - Not interested
	Pyke Electric	Declined	SBE, DBE/MBE	02/21/2022 09:28	01-06-2022 11:30 AM Juna Hagaman said: Will respond to email., 01-06-2022 11:31 AM Juna Hagaman said: Will respond to email., 02-25-2022 9:34 AM Sebastian Fonnegra said: No answer - Not interested
	SAJO MANAGEMENT GROUP LLC DB	Declined	DBE		01-04-2022 10:20 AM Juna Hagaman said: Owner will review tomorrow and respond to email., 02-25-2022 9:22 AM Sebastian Fonnegra said: No answer - Not interested
	The Blue Book	Declined		01/19/2022 12:08	02-25-2022 9:37 AM Sebastian Fonnegra said: No answer - Not interested
	TNA Electric	Declined	SBE-E, DISABLED/SVC DISABLED VET, NECA	01/06/2022 20:54	01-06-2022 11:32 AM Juna Hagaman said: VM, 02-25-2022 9:34 AM Sebastian Fonnegra said: No answer - Not interested
	Triton Electric Company	Declined	SBE		01-06-2022 11:34 AM Juna Hagaman said: Resent to admin., 02-25-2022 9:34 AM Sebastian Fonnegra said: No answer - Not interested
	Universal Electric of Florida	Declined	SBE	01/07/2022 08:21	01-06-2022 11:37 AM Juna Hagaman said: Resent, 01-06-2022 11:38 AM Juna Hagaman said: Resent to Phil, 02-25-2022 9:34 AM Sebastian Fonnegra said: No answer - Not interested
	Valor Construction Management	Declined	SDVOSB, SBA 8(a), FED HUB ZONE		01-06-2022 11:38 AM Juna Hagaman said: VM, 02-25-2022 9:34 AM Sebastian Fonnegra said: No answer - Not interested
	Wright Brothers Contracting Service	Declined			01-04-2022 10:53 AM Juna Hagaman said: Resent to : Vishal Singh vsingh@wrightbrotherscs.com, 02-25-2022 9:32 AM Sebastian Fonnegra said: No answer - Not interested

SECTION F

# Scope Sheets

## Subcontractor Proposals


See Individual Document





SECTION G

# Public Ad

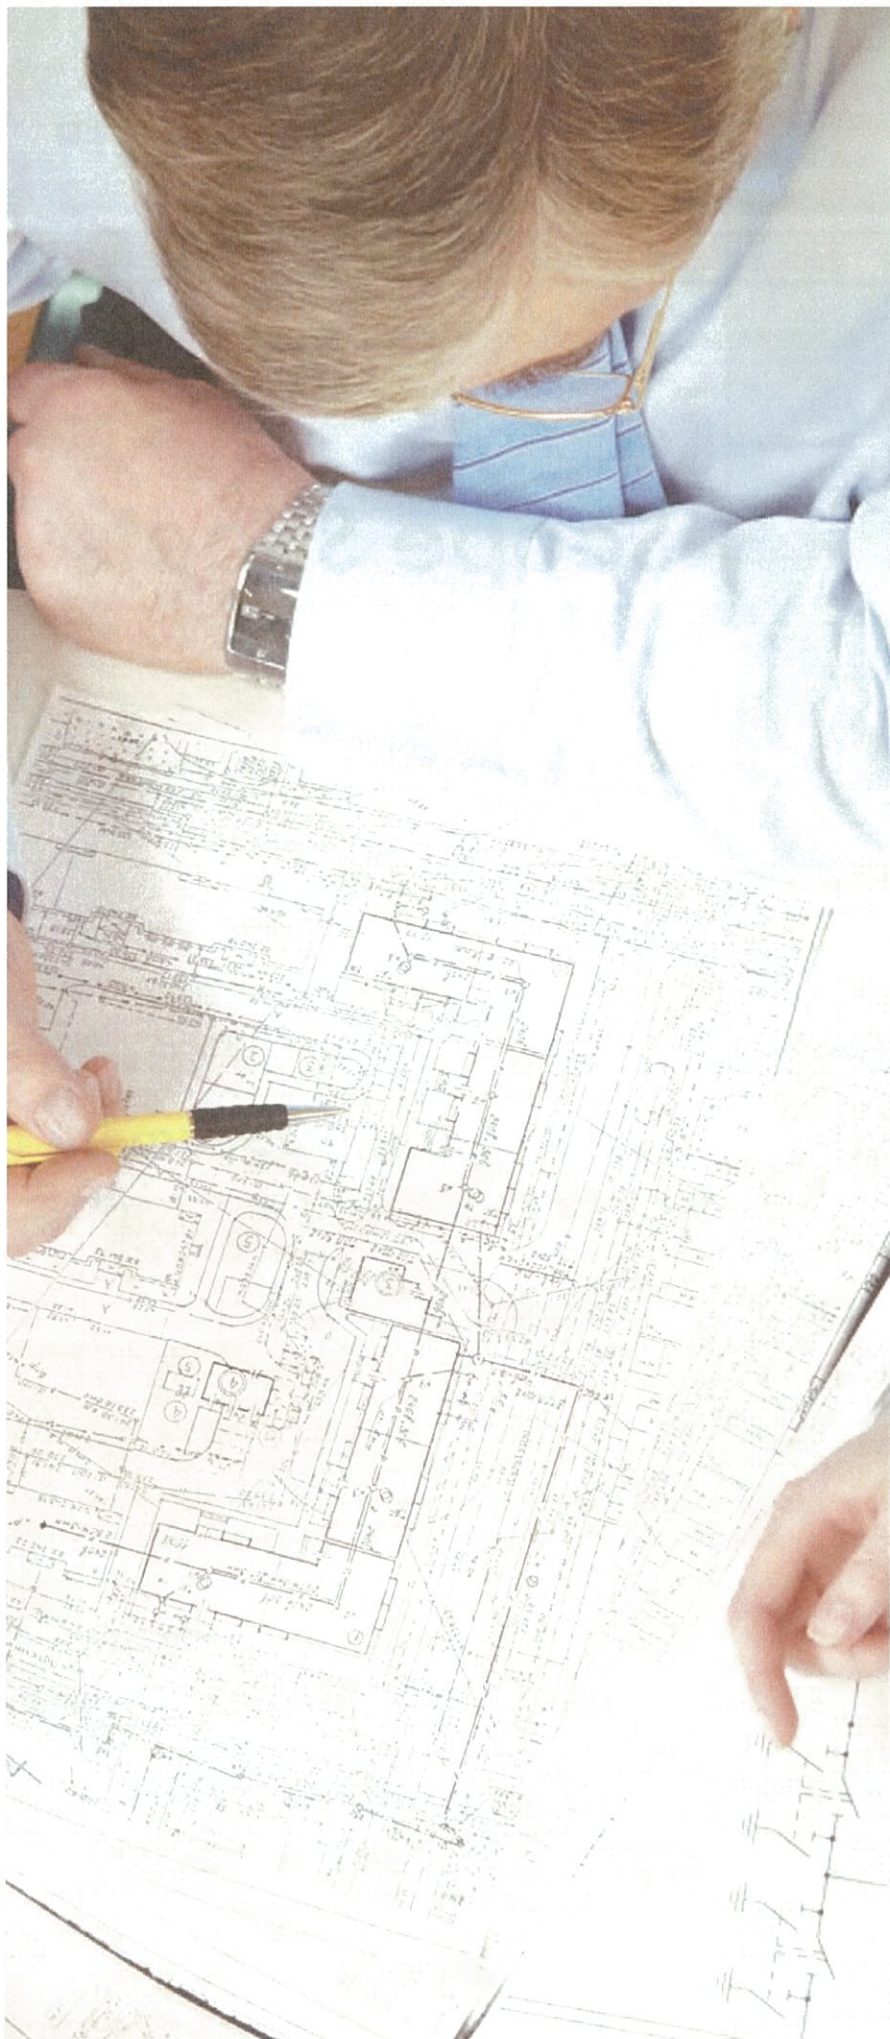

# The Palm Beach Post

Palm Beach Daily News | **LOCAL10**

## PROOF OF PUBLICATION STATE OF FLORIDA


## PUBLIC NOTICE

Before the undersigned authority, personally appeared Teal Pontarelli, who on oath, says that he/she is a Legal Advertising Representative of The Palm Beach Post, a daily and Sunday newspaper, published in West Palm Beach and distributed in Palm Beach County, Martin County, and St. Lucie County, Florida; that the attached copy of advertising for a Legal - Notice to Bid was published in said newspaper in issues dated: first date of Publication 01/05/2022 and last date of Publication 02/04/2022, or by publication on the newspaper's website. Affiant further says that the said The Palm Beach Post is a newspaper published in West Palm Beach, in said Palm Beach County, Florida and that the said newspaper has heretofore been continuously published in said Palm Beach County, Florida, daily and Sunday and has been entered as second class mail matter at the post office in West Palm Beach, in said Palm Beach County, Florida, for a period of one year next preceding the first publication of the attached copy of advertisement; and affiant further says that he/she has neither paid nor promised any person, firm or corporation any discount, rebate, commission or refund for the purpose of securing this advertisement for publication in said newspaper.

LEBOLO CONSTRUCTION MANAGEMENT  
2100 CORPORATE DRIVE  
BOYNTON BEACH, FL 33426

Invoice/Order Number:	0000678868
Ad Cost:	\$3,467.52
Paid:	\$3,467.52
Balance Due:	\$0.00



Signed



(Legal Advertising Agent)

Sworn or affirmed to, and subscribed before me, this 9th day of February, 2022, in Testimony whereof, I have hereunto set my hand and affixed my official seal, the day and year aforesaid.

Signed



Please see Ad on following page(s).

LEBOLO CONSTRUCTION MANAGEMENT  
2100 CORPORATE DRIVE  
BOYNTON BEACH, FL 33426

Invoice/Order Number:	0000678868
Ad Cost:	\$3,467.52
Paid:	\$3,467.52
Balance Due:	\$0.00

ADVERTISEMENT FOR BID 2020-0024  
SLO4 - LEBOLO CONSTRUCTION MANAGEMENT, INC. for Palm Beach County - Department of Airports (Owner) is seeking bids for the project: FIS & Building 846 Storm Resiliency Modifications - Package 2 at Palm Beach International Airport. The overall scope of the project involves rooftop new metal grating and structural steel frame over existing screen wall to protect two (2) new replacement chiller units, chiller WS bench beams replacement, lightning system and antennas temporary relocation, interior structural steel deck reinforcement, VAV boxes replacement, new and repairs of acoustical and hard ceilings. Project bid documents are available via SmartBid. The Pre-Bid Conference and Site Visit are scheduled for 01/12/22 at 1:00 PM at 846 Palm Beach International Airport - West Palm Beach, FL 33406 for all interested subcontractors. Must be limited to one (1) representative per company and must comply with COVID protocols; interested participants are required to wear a face mask at all times, participants will need to undergo a Temperature Screening and Questionnaire before entering the building. Palm Beach County, in accordance with the provisions of Title VI of the Civil Rights Act of 1964 (78 Stat. 252, 42 USC 55 2000d to 2000d-4) and the Regulations, hereby notifies all bidders or offerors that it will affirmatively ensure that any contract entered into pursuant to this advertisement, disadvantaged business enterprises will be afforded full and fair opportunity to submit bids in response to this invitation and will not be discriminated against on the grounds of race, color, or national origin in consideration for an award. Preference will be given to firms having a permanent place of business in Palm Beach County as per Local Preferences (Article 2-2.1.13.2). Sealed Bids must be submitted on or before February 8, 2022, 02:00 PM at 846 Palm Beach International Airport, West Palm Beach, FL 33406 on a sealed envelope with your Company Name, Date, and Name of the Project. Electronic mail proposals are not accepted for this solicitation. No bid may be withdrawn after the bid due date & time for a period of 90 days. LEBOLO reserves the right to reject any or all bids & waive any informalities or irregularities in the bids, & to re-advertise for bids for any reason. All costs incurred by bidders in preparing a proposal shall be the sole responsibility of the bidder. For help contact LEBOLO Pre-Construction Office (bids@lebolo.com) 561-742-7644 for access to SmartBid to complete prequal info & access bid docs.  
1-5, 1-7, 1-10, 1-12, 1-14, 1-17, 1-19, 1-21, 1-24, 1-26, 1-28, 1-31, 2-2, 2-4/2022  
0000678868-01



SECTION H

# Drawing Log







Lebolo Construction Management, Inc.

Printed on Wed Mar 9, 2022 at 09:26 am EST  
Job #: 2020-0024 PBIA - Storm Resilience Phase 2  
846 846, Palm Beach International Airport  
West Palm Beach, Florida 33406

### 100% CD's Storm Resilience Pck. (10/08/21)

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
<b>Cover Sheet</b>					
Cover Sheet	COVER SHEET	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
<b>General</b>					
G001	GENERAL NOTES, ABBREVIATIONS AND SYMBOLS & SHEET INDEX	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
G002	GENERAL CONTRACT NOTES & SAFETY AND SECURITY NOTES	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
G003	WORK AREA & ACCESS ROUTE	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
G004	CONSTRUCTION SCHEDULE	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
G100	CONTRACT LAYOUT PLAN AND GENERAL NOTES	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
<b>Architectural</b>					
A131	OVERALL FIRST LEVEL REFLECTED CEILING PLAN	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
A131	OVERALL FIRST LEVEL REFLECTED CEILING PLAN	1	01/03/2022	01/10/2022	100% CD's Storm Resilience Pck. (10/08/21)
A132	OVERALL SECOND LEVEL REFLECTED CEILING PLAN	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
A132	OVERALL SECOND LEVEL REFLECTED CEILING PLAN	1	01/03/2022	01/10/2022	100% CD's Storm Resilience Pck. (10/08/21)
A132A	PARTIAL SECOND LEVEL REFLECTED CEILING PLAN	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
A132A	PARTIAL SECOND LEVEL REFLECTED CEILING PLAN	1	01/03/2022	01/10/2022	100% CD's Storm Resilience Pck. (10/08/21)
<b>Electrical</b>					
E001	ELECTRICAL GENERAL NOTES, SYMBOLS, AND ABBREVIATIONS	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
E101	OVERALL FIRST FLOOR POWER PLAN	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
E102	OVERALL SECOND FLOOR POWER PLAN	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
E103	OVERALL ROOF LEVEL POWER PLAN	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
E801	PARTIAL ELECTRICAL ONE-LINE DIAGRAM	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
E901	EXISTING PANELBOARD SCHEDULES	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)



Lebolo Construction Management, Inc.

Printed on Wed Mar 9, 2022 at 09:26 am EST

Job #: 2020-0024 PBIA - Storm Resilience Phase 2  
846 846, Palm Beach International Airport  
West Palm Beach, Florida 33406

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
ED101	OVERALL FIRST FLOOR ELECTRICAL DEMOLITION PLAN	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
ED102	OVERALL SECOND FLOOR ELECTRICAL DEMOLITION PLAN	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
ED103	OVERALL ROOF LEVEL ELECTRICAL DEMOLITION PLAN	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
ED103	OVERALL ROOF LEVEL ELECTRICAL DEMOLITION PLAN	1	01/03/2022	01/10/2022	100% CD's Storm Resilience Pck. (10/08/21)
<b>Mechanical</b>					
M001	LEGEND AND GENERAL NOTES	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
M101	OVERALL FIRST FLOOR HVAC PLAN	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
M102	OVERALL SECOND FLOOR HVAC PLAN	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
M103A	PARTIAL ROOF HVAC PLAN - AREA A	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
M103A	PARTIAL ROOF HVAC PLAN - AREA A	1	01/03/2022	01/10/2022	100% CD's Storm Resilience Pck. (10/08/21)
M201	CHILLER PIPING SCHEMATIC	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
M501	MECHANICAL DETAILS	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
M601	MECHANICAL HVAC SCHEDULE	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
M701	MECHANICAL CONTROLS	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
M702	MECHANICAL CONTROLS	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
M703	MECHANICAL CONTROLS	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
MD101	OVERALL FIRST FLOOR HVAC DEMOLITION PLAN	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
MD102	OVERALL SECOND FLOOR HVAC DEMOLITION PLAN	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
MD103A	PARTIAL ROOF HVAC DEMOLITION PLAN - AREA A	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)
MD103A	PARTIAL ROOF HVAC DEMOLITION PLAN - AREA A	1	01/03/2022	01/10/2022	100% CD's Storm Resilience Pck. (10/08/21)
<b>Structural</b>					
S101	STRUCTURAL NOTES, PLANS, AND DETAILS	0	10/08/2021	10/21/2021	100% CD's Storm Resilience Pck. (10/08/21)




SECTION I

# Construction Schedule





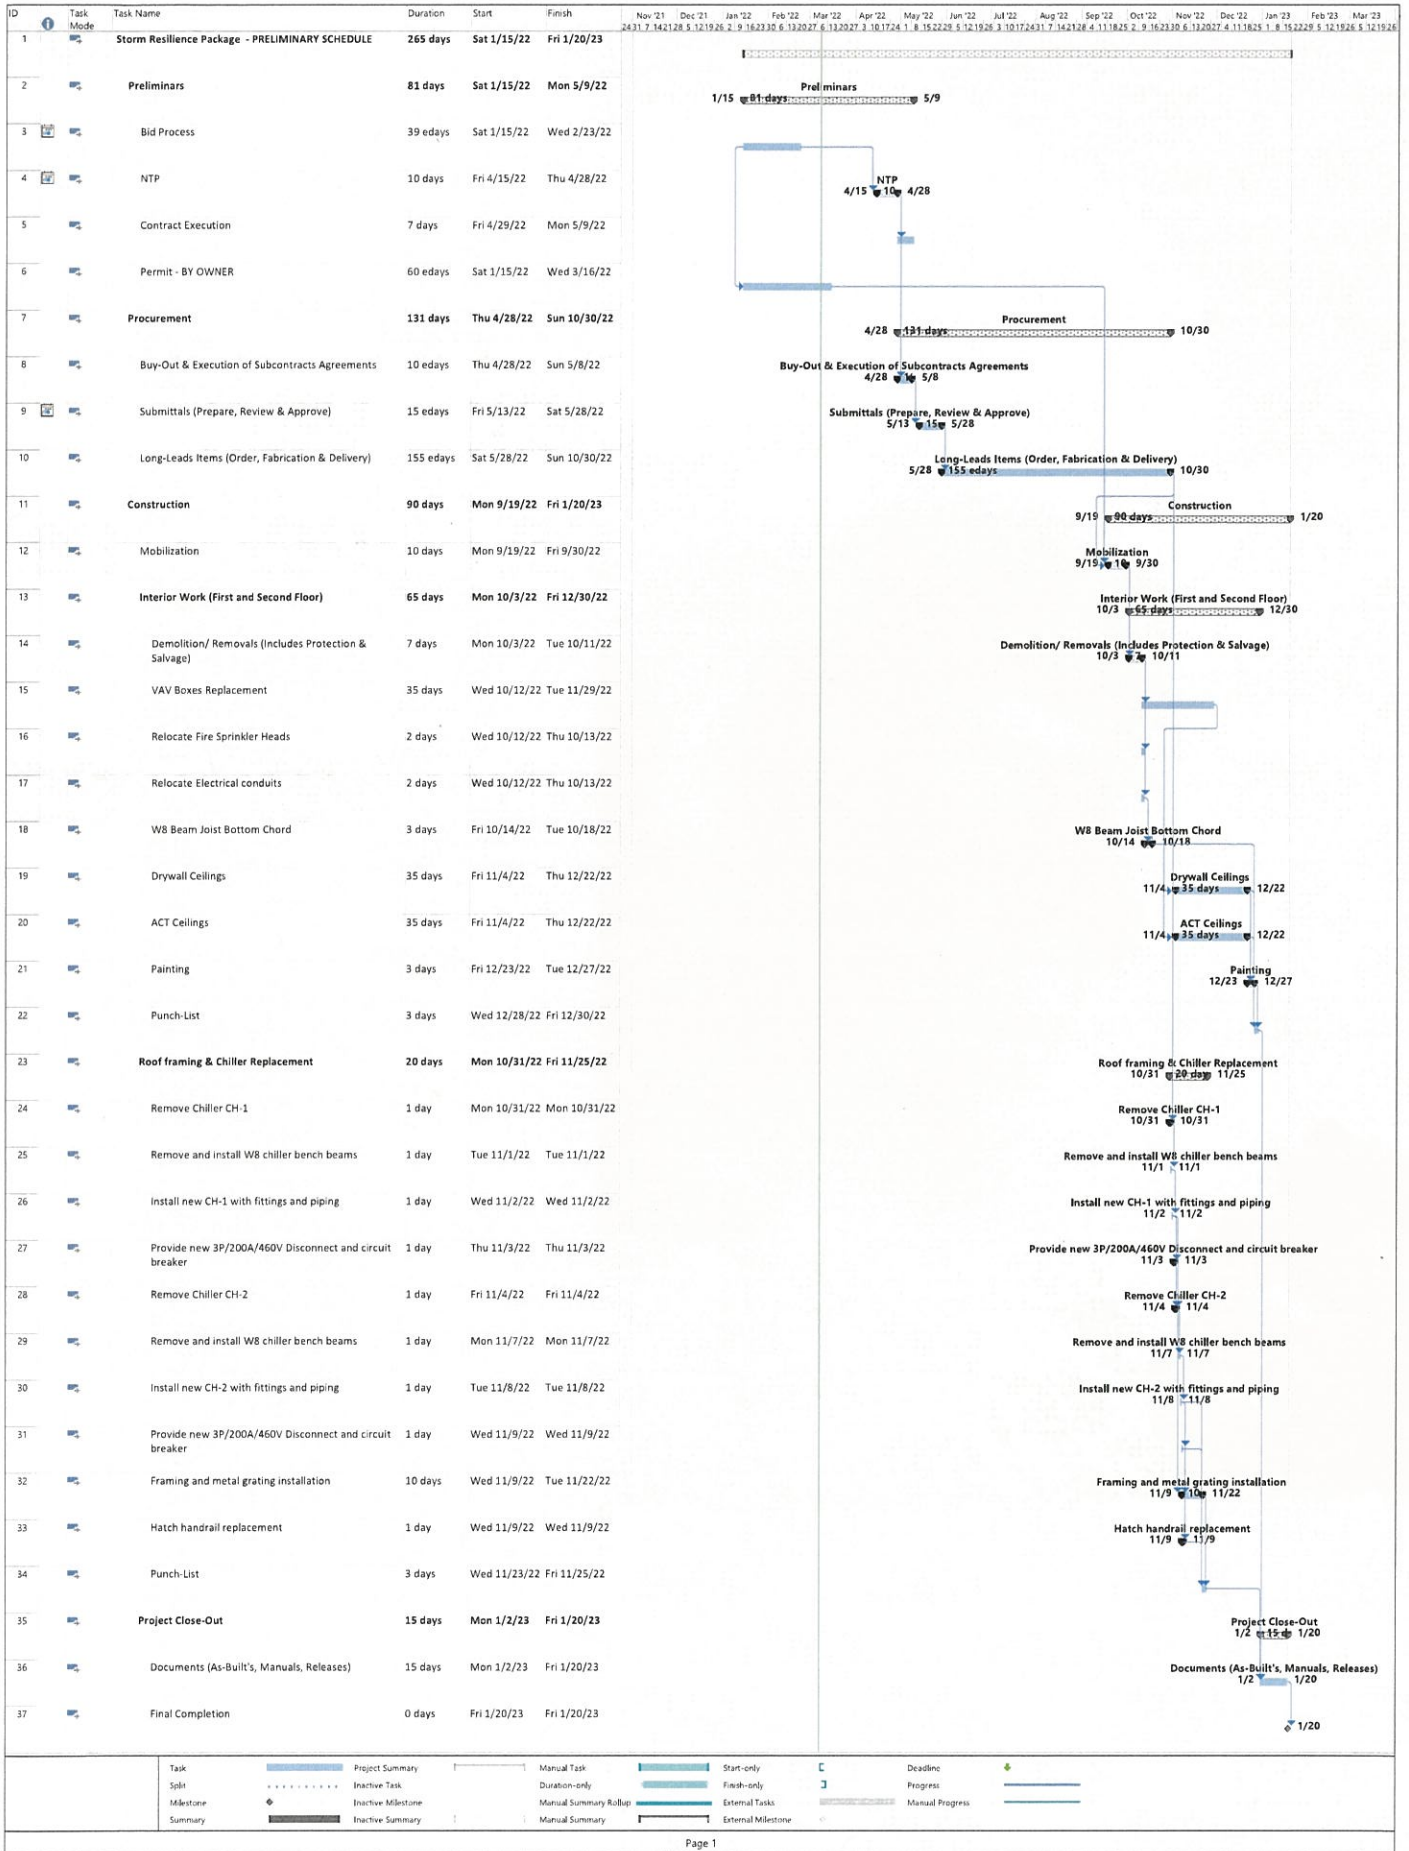

SECTION J

# Site Visit Attendance

## Bid Opening Log







**Subcontractors  
PreBid Meeting & Site Visit Attendance**

PROJECT NAME :

SL-04 FIS & BUILDING 846 STORM  
RESILIENCY MODIFICATIONS PACKAGE 2

LEBOLO PROJECT No:

2021-0024

PBIA PROJECT No:

DOA 18-2A SL-04

VERSION:

1.0

SITE VISIT DATE:

Wednesday, January 12, 2022

FORM LCM-PC-17 | 08/20/2021

**PALM BEACH COUNTY DEPARTMENT OF AIRPORTS**

Name	Company	Signature
WARD HOOR	Big Air Mechanical	[Signature]
	Sunshine State	[Signature]
Timothy Sullivan	Palm Beach Iron	[Signature]
	Structural & Metal Services	
	Yats Construction	
	I.Q. Constructions	
Tom Nix	N & P Construction and Development, Inc.	[Signature]
Motaseem Majdalawi	Cedars Electro-Mechanical	[Signature]
Edens Vilma	Van Linda Iron Works	[Signature]
PATRICK GORDON	QUANTUM MECHANICAL	[Signature]
Daren Gordon	Quantum Mechanical	[Signature]
GEORGE SANTOS	PBCDOA	[Signature]
Tim Uff	Florida Mech	[Signature]
SEBASTIAN FERRER	LEBOLO	[Signature]
Everton Whitch	Everton Electric	[Signature]

SEE  
DRAWINGS





# BID OPENING LOG

PROJECT NAME :	SL-04 FIS & BUILDING 846 STORM RESILIENCY MODIFICATIONS PACKAGE 2
LEBOLO PROJECT No:	2021-0024
PBIA PROJECT No:	DOA 18-2A SL-04
OPENING DATE:	Tuesday, February 8, 2022
OPENING TIME:	2:00 PM

FORM LCM-PC-21 | 10/19/2021

## PALM BEACH COUNTY DEPARTMENT OF AIRPORTS

Company Name	Trade (s)	Bid Form (Yes/No)	Amount USD
CEDARS ELECTRO MECHANICAL HVAC		YES.	\$ 681,315 HVAC \$ 12,500 TEMP HVAC BOLD \$ 14,160. MONTH.
VAN LINDA IRON WORKS. S. STEEL.		YES	\$ 176,191.16
QUANTUM MECHANICAL HVAC		YES.	\$ 569,000.00.
FLORIDA MECHANICAL HVAC		YES.	\$ 702.485.00.
T.W.S. FABRICATORS S. STEEL		NO	\$ 174,000.00.
FARMER & IRWING HVAC		YES.	\$ 566,673 (1 WEEK) \$ 563,658 (1 MONTH) BOLD \$ 7272.00.
N & P CONSTRUCTION SELECTIVE DEMO		YES.	\$ 73,700.00.

PALM BEACH COUNTY DEPARTMENT OF AIRPORTS		LEBOLO CONSTRUCTION MANAGEMENT, INC.	
By:		By:	
Print Name: GEORGE SANTOS		Print Name: SEBASTIAN FOULGER	
Title: PROJECT ENGINEER Date: 2/8/2022		Title: Pre-CON MANAGER Date: 2/8/22.	

SECTION K

# **Constructability Report**

## **VA/VE Report**





# CONSTRUCTABILITY LOG

## PRE-CONSTRUCTION

LEBOLO PROJECT No: 2021-0024  
PBIA PROJECT No: DOA 18-2A SL-04  
VERSION: 1.0  
DATE: Wednesday, December 15, 2021

FORM LCMPC-03 09/21/2021

### PALM BEACH COUNTY DEPARTMENT OF AIRPORTS SL-04 FIS & BUILDING 846 STORM RESILIENCY MODIFICATIONS PACKAGE 2

REVIEWER NAME	REVIEWER FIRM	SPEC. SECTION & DWG #	TRADE	ACTIVITY	SITUATION	RECOMMENDATION	COST IMPACT	RESPONSE FROM	RESPONSE	ACTION	IMPACT DRAWINGS	IMPACT SPECS
Sebastian Fonnegra	LEBOLO	N/A	Mechanical	Replace chiller units CH-1 & CH-2	The area around Adm. Bldg. does not allow sufficient space to stage the crane without impacting vehicular traffic	Crane can be staged SW of Adm. Bldg. inside airport area. Special permission may be required	N/A	Aaron Jackson	Accepted	Included in 100% CDs	Yes	No
Sebastian Fonnegra	LEBOLO	N/A	Mechanical	Replace chiller units CH-1 & CH-2	Height of boom crane must be verified due to the possibility of airport restrictions	During the Precon phase request input from the supplier	N/A	Sunshine State and Farmer & Irwin	Use a 150Ton crane to be on the safe loading zone. Boom lift was verified	Crane can be used without interfering airport operations	No	No
Sebastian Fonnegra	LEBOLO	N/A	S. Steel Misc. Metals	Chiller bench W8 beams replacement and new metal grating installation	Material size must be verified to allow access through the existing roof hatch	Field coordination will be implemented to use same crane for chiller and metals	No Impact	Sunshine State and Farmer & Irwin	Field coordination to use same crane is possible	HVAC crane will bring materials to rooftop	No	No
Sebastian Fonnegra	LEBOLO	024119 - Selective Demolition A131, A132	Selective Demolition Acoustical Ceiling	Acoustical ceiling removal for VAV Replacement	On previous projects we had to partially remove AC grid with the inconvenience of having the existing remaining grid damaged on the edges causing additional cost to replace the entire areas to comply with QC	Remove complete AC grid in each room to avoid future cost implications or include an allowance for additional repairs if needed	TBD	Nicholas Hopkins	REMOVE AND REPLACE: Demolish entire existing ACT ceiling and grid in full room. Provide all new framing system and tiles. Rooms: 108 - Multi-Purpose Room, 113 - Employee Break Room, 116 - Emergency Supply Storage, 141 - Plans Review, 144 - I.T. Mgr., 147 - Laboratory, 148 - Server, 203 - Fiscal Spec II, 213 - Conference Rm., 217 - Conference Rm., 235 - Data, 240 - Plan Storage, & 241 - File Storage REMOVE AND REINSTALL: Demolish main and secondary framing to limits shown in plans. Provide new main and secondary framing lying into existing to remain. Re-install existing tiles to maintain color consistency in the corridor. Rooms: All Corridors, 219 - Central Storage	Included in Addendum 1	YES	NO
Sebastian Fonnegra	LEBOLO	055313 S-101	S. Steel	New W8 below joist bottom chord	There is an access restriction to get the proposed 22ft long W8 into the second floor of the building	Design W8 as two components to be mechanically attached for final installation	TBD	Aaron Jackson	Agreed. Note on 7/5101 indicates for the beam to be spliced mid-span between joists (approx 13'-3" / 8'-9" split). Note indicates splice shall be fully bolted and designed for full shear and moment capacity.	Included in 100% CDs		
Sebastian Fonnegra	LEBOLO	MD101, MD102, M101, M102	Selective Demolition Acoustical Ceiling Mechanical Electrical	VAV replacement	The work requires to install new VAV units in occupied space	Coordinate with PBIA Adm. to relocate personnel or plan for afterhours & weekends work to avoid conflicts	N/A	Aaron Jackson	No exception taken to recommendation. Note that demolition is required to be completed at nighttime per General Contract Note #22 on G002. New installation work shall be coordinated with airport staff.	Included in 100% CDs		



# VAVE LOG

## PRE-CONSTRUCTION

LEBOLO PROJECT No:	2021-0024
PBIA PROJECT No:	DOA 18-2A SL-04
VERSION:	1.0
DATE:	Wednesday, December 15, 2021


FORM LCM-PC-19 | 09/21/2021

### PALM BEACH COUNTY DEPARTMENT OF AIRPORTS SL-04 FIS & BUILDING 846 STORM RESILIENCY MODIFICATIONS PACKAGE 2

REVIEWER NAME	REVIEWER FIRM	SPEC. SECTION & DWG #	VAVE COMMENT	DISCIPLINES IMPACTED	COST IMPACT	RESPONSE FROM	RESPONSE	ACTION	CHANGE IMPACT DRAWINGS	CHANGE IMPACT SPECS
Sebastian Fornegra	LEBOLO	055313 S-101	Existing supports for antennas are located on the interior of the enclosure. If new metal grating has a detail to surround each support, this should be considered as an alternate to leave antenna's supports were they exist and reduce the cost associated with this relocation	Misc. Metals Communications	TBD	Aaron R Jackson	Agreed. See Note on photo near Section 3 of S101. Note states that horizontal leg of L3x3 of 3/8"101 and grating shall be coped at existing antenna support posts and to provide 1" clearance. Note on 6/S101 indicates that Antenna's are to remain active while installation occurs but can be relocated at Contractor's option.	None needed. Info included on 100% CD's.	YES	NO
Sebastian Fornegra	LEBOLO	M-601	VAV and Chiller Units are specified by Trane. Considering alternate manufacturers may result in savings	Mechanical	TBD	Kevin Gomez	Chillers and VAV boxes equal to those specified will be considered; however, any and all costs required due to alternates shall be included. This includes but not limited to controls integration to the existing system and any electrical modifications necessary. The controls shall remain on the native Trane controls network including compatible hardware and software & matching protocol.		YES	NO



# **Public Construction Bond**



NIELSON, HOOVER & COMPANY



March 29, 2022

Palm Beach County Board of County Commissioners  
c/o Dept. of Airports  
846 Palm Beach International Airport  
West Palm Beach, FL 33406-1470

**RE:**      **Authority to Insert Contract Date and Date Bond(s) and**  
         **Power(s) of Attorney**  
         **Principal:      Lebolo Construction Management, Inc.**  
         **Bond No.      6021361629**  
         **Project:      SL 04 FIS & Building 846 Storm Resiliency Modifications Package 2 - SL 04**

To Whom It May Concern:

Please be advised that this letter serves as our authorization for Palm Beach County Board of County Commissioners c/o Dept. of Airports to do the following:

- *Once the Contract is signed, insert the date of the contract to the bond(s);*
- *Date the bond(s) and Power(s) of Attorney the date of the contract; and*

Please provide us with a copy for our files.

If you have any questions, please do not hesitate to contact this office.

Sincerely yours,

NIELSON, HOOVER & ASSOCIATES

Charles J. Nielson  
President of Nielson, Hoover & Associates and,  
Attorney-In-Fact of United States Fire Insurance Company

Attachments



**PUBLIC CONSTRUCTION BOND**

BOND NUMBER 6021361629

BOND AMOUNT One Million Five Hundred Eighteen Thousand Seven Hundred Ninety and 48/100 Dollars (\$1,518,790.48)

CONTRACT AMOUNT One Million Five Hundred Eighteen Thousand Seven Hundred Ninety and 48/100 Dollars (\$1,518,790.48)

CONTRACTOR'S NAME: Lebolo Construction Management, Inc.

CONTRACTOR'S ADDRESS: 2100 Corporate Drive, Boynton Beach, FL, 33426

CONTRACTOR'S PHONE: (561) 742-7644

SURETY COMPANY: United States Fire Insurance Company

SURETY'S ADDRESS: 305 Madison Avenue, Morristown, NJ 07960

SURETY'S PHONE: (973) 490-6600

OWNER'S NAME: PALM BEACH COUNTY BOARD OF COUNTY COMMISSIONERS

OWNER'S ADDRESS: c/o Department of Airports  
846 Palm Beach International Airport  
West Palm Beach, Florida 33406-1470

OWNER'S PHONE: (561) 471-7462

PROJECT NAME: SL 04 FIS & Building 846 Storm Resiliency Modifications Package 2

PROJECT NUMBER: SL 04

CONTRACT NUMBER (to be provided after Contract award): R-2022-0457

DESCRIPTION OF WORK: 2 Rooftop Chiller units replacement, new grating over chillers, replace chiller support beams, Interior (35) VAV replacements, Acoustical Ceiling replacement, Interior W8 Steel Beam installation.

PROJECT ADDRESS, PCN, or LEGAL DESCRIPTION: 846 Palm Beach International Airport, West Palm Beach, FL 33406

Legal Description: PCN 00-43-43-31-01-001-0010

This Bond is issued in favor of the County conditioned on the full and faithful performance of the Contract.

KNOW ALL MEN BY THESE PRESENTS: that Contractor and Surety, are held and firmly bound unto

Palm Beach County Board of County Commissioners  
301 N. Olive Avenue  
West Palm Beach, Florida 33401

as Oblige, herein called County, for the use and benefit of claimant as herein below defined, in the amount of

One Million Five Hundred Eighteen Thousand Seven Hundred Ninety and 48/100 Dollars (\$1,518,790.48)  
(Here insert a sum equal to the Contract Price)

for the payment whereof Principal and Surety bind themselves, their heirs, personal representatives, executors, administrators, successors and assigns, jointly and severally, firmly by these presents.

WHEREAS,

Principal has by written agreement entered into a contract with the County for

Project Name: FIS & Building 846 Storm Resiliency Modifications Package 2  
Project No.: SL 04  
Project Description: 2 Rooftop Chiller units replacement, new grating over chillers, replace chiller support beams, Interior (35) VAV replacements, Acoustical Ceiling replacement, Interior W8 Steel Beam installation.  
Project Location: 846 Palm Beach International Airport, West Palm Beach, FL 33406

in accordance with Drawings and Specifications prepared by

NAME OF ARCHITECTURAL FIRM: RS&H  
LOCATION OF FIRM: 3125 West Commercial Blvd, Suite 130, Fort Lauderdale, FL, 33309.  
PHONE: (954) 474-3005

NAME OF ARCHITECTURAL FIRM: JLRD Consulting Engineers  
LOCATION OF FIRM: 1450 Centrepark Boulevard, Suite 350, West Palm Beach, Fl, 33401  
PHONE: (561) 689-2303

which contract is by reference made a part hereof in its entirety and is hereinafter referred to as the Contract.



THE CONDITION OF THIS BOND is that if Principal:

1. Performs the contract between Principal and County for the construction of SL 04 FIS & Building 846 Storm Resiliency Modifications Package 2, the contract being made a part of this bond by reference, at the times and in the manner prescribed in the contract; and
2. Promptly makes payments to all claimants, as defined in Section 255.05, Florida Statutes, supplying Principal with labor, materials, or supplies, used directly or indirectly by Principal in the prosecution of the work provided for in the contract; and
3. Pays County all losses, damages (including liquidated damages), expenses, costs, and attorneys' fees, including appellate proceedings, that County sustains because of a default by Principal under the contract; and
4. Performs the guarantee of all work and materials furnished under the contract for the time specified in the contract, then this bond is void; otherwise it remains in full force.
5. Any changes in or under the contract documents and compliance or noncompliance with any formalities connected with the contract or the changes does not affect Surety's obligation under this bond and Surety waives notice of such changes.
6. The amount of this bond shall be reduced by and to the extent of any payment or payments made in good faith hereunder, inclusive of the payment by Surety of construction liens which may be filed of record against said improvement, whether or not claim for the amount of such lien be presented under and against the bond.
7. Principal and Surety expressly acknowledge that any and all provisions relating to consequential, delay and liquidated damages contained in the contract are expressly covered by and made a part of this Performance, Labor and Material Payment Bond. Principal and Surety acknowledge that any such provisions lie within their obligations and within the policy coverages and limitations of this instrument.

Section 255.05, Florida Statutes, as amended, together with all notice and time provisions contained therein, is incorporated herein, by reference, in its entirety. Any action instituted by a claimant under this bond for payment must be in accordance with the notice and time limitation provisions in Section 255.05(2), Florida Statutes. This instrument regardless of its form, shall be construed and deemed a statutory bond issued in accordance with Section 255.05, Florida Statutes.

Any action brought under this instrument shall be brought in the court of competent jurisdiction in Palm Beach County and not elsewhere.

Dated: May 3, 2022

Witness

Andria Powell

Print Name

Witness

Charles D. Nielson

Print Name

Lebolo Construction Management, Inc.

Principal

(Seal)

Pre-Construction MNG.

Title

United States Fire Insurance Company

Surety

(Seal)

Charles D. Nielson

Title – Attorney-In-Fact

***Bond Must Contain Original Signatures.  
No Copies Will Be Accepted***

IMPORTANT: Surety companies executing bonds must appear and remain on the U.S. Treasury Department's most current list (Federal Register) during construction, guarantee and warranty periods, and be authorized to transact business in the State of Florida.

The provisions and limitations of Section 255.05 Florida Statutes, including but not limited to the notice and time limitations in Sections 255.05(2) and 255.05(10), are incorporated in this bond by reference.



**POWER OF ATTORNEY  
UNITED STATES FIRE INSURANCE COMPANY  
PRINCIPAL OFFICE - MORRISTOWN, NEW JERSEY**

0092722

**KNOW ALL MEN BY THESE PRESENTS:** That United States Fire Insurance Company, a corporation duly organized and existing under the laws of the state of Delaware, has made, constituted and appointed, and does hereby make, constitute and appoint:

*Ian A. Nipper, David Russell Hoover, Joseph Penichet Nielson,  
Charles David Nielson, Charles Jackson Nielson, Shawn Alan Burton, Jarrett Merlucci*

each, its true and lawful Attorney(s)-In-Fact, with full power and authority hereby conferred in its name, place and stead, to execute, acknowledge and deliver: Any and all bonds and undertakings of surety and other documents that the ordinary course of surety business may require, and to bind United States Fire Insurance Company thereby as fully and to the same extent as if such bonds or undertakings had been duly executed and acknowledged by the regularly elected officers of United States Fire Insurance Company at its principal office, in amounts or penalties not exceeding: **Seven Million, Five Hundred Thousand Dollars (\$7,500,000).**

This Power of Attorney limits the act of those named therein to the bonds and undertakings specifically named therein, and they have no authority to bind United States Fire Insurance Company except in the manner and to the extent therein stated.

This Power of Attorney revokes all previous Powers of Attorney issued on behalf of the Attorneys-In-Fact named above and expires on January 31, 2023.

This Power of Attorney is granted pursuant to Article IV of the By-Laws of United States Fire Insurance Company as now in full force and effect, and consistent with Article III thereof, which Articles provide, in pertinent part:


Article IV, Execution of Instruments - Except as the Board of Directors may authorize by resolution, the Chairman of the Board, President, any Vice-President, any Assistant Vice President, the Secretary, or any Assistant Secretary shall have power on behalf of the Corporation:

- (a) to execute, affix the corporate seal manually or by facsimile to, acknowledge, verify and deliver any contracts, obligations, instruments and documents whatsoever in connection with its business including, without limiting the foregoing, any bonds, guarantees, undertakings, recognizances, powers of attorney or revocations of any powers of attorney, stipulations, policies of insurance, deeds, leases, mortgages, releases, satisfactions and agency agreements;
- (b) to appoint, in writing, one or more persons for any or all of the purposes mentioned in the preceding paragraph (a), including affixing the seal of the Corporation.

Article III, Officers, Section 3.11, Facsimile Signatures. The signature of any officer authorized by the Corporation to sign any bonds, guarantees, undertakings, recognizances, stipulations, powers of attorney or revocations of any powers of attorney and policies of insurance issued by the Corporation may be printed, facsimile, lithographed or otherwise produced. In addition, if and as authorized by the Board of Directors, dividend warrants or checks, or other numerous instruments similar to one another in form, may be signed by the facsimile signature or signatures, lithographed or otherwise produced, of such officer or officers of the Corporation as from time to time may be authorized to sign such instruments on behalf of the Corporation. The Corporation may continue to use for the purposes herein stated the facsimile signature of any person or persons who shall have been such officer or officers of the Corporation, notwithstanding the fact that he may have ceased to be such at the time when such instruments shall be issued.

**IN WITNESS WHEREOF,** United States Fire Insurance Company has caused these presents to be signed and attested by its appropriate officer and its corporate seal hereunto affixed this 28<sup>th</sup> day of September, 2021.

**UNITED STATES FIRE INSURANCE COMPANY**




Matthew E. Lubin, President

State of New Jersey }  
County of Morris }

On this 28<sup>th</sup> day of September, 2021, before me, a Notary public of the State of New Jersey, came the above named officer of United States Fire Insurance Company, to me personally known to be the individual and officer described herein, and acknowledged that he executed the foregoing instrument and affixed the seal of United States Fire Insurance Company thereto by the authority of his office.

**MELISSA H. D'ALESSIO**  
NOTARY PUBLIC OF NEW JERSEY  
Commission # 60125633  
My Commission Expires 4/1/2025



Melissa H. D'Alessio

(Notary Public)

I, the undersigned officer of United States Fire Insurance Company, a Delaware corporation, do hereby certify that the original Power of Attorney of which the foregoing is a full, true and correct copy is still in force and effect and has not been revoked.

**IN WITNESS WHEREOF,** I have hereunto set my hand and affixed the corporate seal of United States Fire Insurance Company on the 3<sup>rd</sup> day of May 2022.

**UNITED STATES FIRE INSURANCE COMPANY**



Alfred N. Wright, Senior Vice President

## Contract History



DEPARTMENT OF AIRPORTS  
MISCELLANEOUS AIRPORT IMPROVEMENTS - CMAR (LOCAL O&EO PROGRAM)  
LEBLO CONSTRUCTION MANAGEMENT INC.  
CONTRACT NO. 18-131  
CONTRACT HISTORY

CONTRACT HISTORY																		
ORIGINAL CONTRACT RESOLUTION NO DATE APPROVED SBE Goal EXPIRATION																		
YEAR 1.2 R-2019-1222 8/20/2019 15.00% 8/20/2021																		
1 <sup>st</sup> EXT YR 3 R2021-0888 7/13/21																		
2 <sup>nd</sup> EXT YR 4 8/20/2023																		
3 <sup>rd</sup> EXT YR 5 8/20/2024																		
AP/GSC	REF DOC	SBE/WMBE PARTICIPATION		DESCRIPTION	TIME(Cal Days) for Substantial	NTP	Substantial Completion Date	Final Completion Date	AMOUNT	CHANGE ORDER OR ADJUSTMENT	CHANGE ORDER VALUE PLUS TIME	REVISED AMOUNT	LEAD DEPT APPROVAL	CRC APPROVAL	BCC APPROVAL	STATUS	TOWO CLOSED	
		Total SBE/WBE (\$)	% SBE															
N/A Under \$100k	Task Order SL-01		0%	Precon for New Noise Monitoring Station at PBI	30	11/26/19			\$1,500.00			\$1,500.00	\$ 1,500.00				Approved 11/26/19	
N/A Under \$100k	Work Order SL-02		0%	Noise Monitor - GMP	60	3/10/20	5/8/20	6/7/20	\$18,160.00			\$16,278.04	\$ 18,160.00					Approved Close-out by COA on 5/19/2020
				GMP Adjustments						(\$1,081.96)								
Waiver - 0%	Work Order SL-03		Waiver	Storm Resiliency Package 1	90	6/10/20	9/7/20	10/7/20	\$168,325.00					0.00			Approved by CRC on 6/10/2020	
				CO No 1	46		10/23/20	11/23/20		\$0.00							Approved 9/9/2020	
				GMP Adjustments						(\$8,377.92)		\$159,847.08					Approved by CRC 2/24/2021	
Amendment 1 Time Extension																		
N/A Under \$100k	Task Order SL-06		15%	Preconstruction Services for Terminal Building 4th Level Exterior Wall Repairs					\$14,644.92			\$14,644.92	\$14,644.92		7/13/21 Board Meeting	Approved 9/21/21		
20% SBE Goal	Amendment 2: SL 07	\$248,297.60	32%	Construction Services for Terminal Building 4th Level Exterior Wall Repairs	211	2/14/22	9/12/22	10/12/22	\$777,546.69						\$777,546.69	Approved R-2022-0135		
				CO No 1	0					\$33,698.89			\$33,698.89					
				GMP Adjustments								\$811,245.58						
20% w/ 1% AANA	Amendment 3: SL 04	\$921,435.00	60%	PreCon & Construction Services for Storm Resiliency Package 2	260				\$1,518,790.48							\$1,518,790.48	Going to May 2nd Board Meeting	
Total									\$2,488,867.09	\$23,439.01	\$1,003,616.62	\$88,003.61	\$0.00	\$2,288,337.17				

Notes:

Items in Blue are (in)

Approval Authority for Task Authorizations (CM @ Risk) - No cumulative tracking

Task Order

Task Order

Task Order

Amendment

Authority

Lead Dept

CRC

BCC

Less than \$100,000

\$100,000 - \$200,000

> \$200,000

Approval Authority

CRC

Lead Dept

BCC

See Note 1

See Note 1

See Note 1

Days

0-30 days

31-60

61-90

91-120

121+

Authority

Lead Dept

CRC

BCC

Cumulative Days up to 30

Individual Days up to 30

See Note 2

Time Extensions in excess of 90 Days must be approved by the Board and does not count towards the

When the cumulative value of changes or additional work approved by the Lead or CRC exceeds the greater of \$250,000 or 5% of the original contract an agenda item notifying the board that the item puts it in the excess category must be prepared and forwarded as a Resiliency and P&E item

When the cumulative time extension approved by a combination of the Lead Dept and the CRC exceeds 120 Cal Days then an agenda item notifying the board that the item puts it in the excess category must be prepared and forwarded as a Resiliency and P&E item

\*Time must also be evaluated based on value of LD's for projects over \$1,000,000. The value of the time extension is not included when calculating the cumulative value

## **Attachment No. 2**

### **OEBO Schedules**



OEBO SCHEDULE 1

LIST OF PROPOSED CONTRACTOR/CONSULTANT AND SUBCONTRACTOR/SUBCONSULTANT PARTICIPATION  
FIS & Building 846 Storm Resiliency Modifications Package 2

SOLICITATION/PROJECT/BID NAME:

SOLICITATION/PROJECT/BID No.:DOA 18-13 (SL-04)

NAME OF PRIME RESPONDENT/BIDDER:Lebolo Construction Management, Inc

ADDRESS:2100 Corporate Drive, Boynton Beach, FL 33426

CONTACT PERSON:Sebastian Fonnegra

PHONE NO.:(561) 742 7644

E-MAIL:sfonnegra@lebolo.com

SOLICITATION OPENING/SUBMITTAL DATE:N/A

DEPARTMENT:PreConstruction

PLEASE LIST THE DOLLAR AMOUNT OR PERCENTAGE OF WORK TO BE COMPLETED BY THE PRIME CONTRACTOR/CONSULTANT ON THIS PROJECT.  
PLEASE ALSO LIST THE DOLLAR AMOUNT OR PERCENTAGE OF WORK TO BE COMPLETED BY ALL SUBCONTRACTORS/SUBCONSULTANTS ON THE PROJECT.

Name, Address and Phone Number		(Check all Applicable Categories)					DOLLAR AMOUNT OR PERCENTAGE OF WORK			
		Non-SBE	M/WBE	SBE	Minority/Women Business	Small Business				
1. All American Ceilings		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>						\$31,988.00
2. Van Linda Iron		<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>						\$210,788.00
3. I.Q. Constructions		<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>					\$39,750.00	
4. Johnson's Controls		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>						\$3,685.83
5. Quantum Mechanical		<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>				\$637,296.00		

(Please use additional sheets if necessary)

Total see P.2

Total see P.2


see P.2

see P.2

Total Bid Price \$1,518,790.48

Total SBE - M/WBE Participation see P.2

I hereby certify that the above information is accurate to the best of my knowledge:



Signature

PreConstruction Manager

Title

Note:

1. The amount listed on this form for a Subcontractor/subconsultant must be supported by price or percentage listed on the properly executed Schedule 2 or attached signed proposal.

2. Firms may be certified by Palm Beach County as an SBE and/or an M/WBE. If firms are certified as both an SBE and/or M/WBE, please indicate the dollar amount under the appropriate category.

3. Modification of this form is not permitted and will be rejected upon submittal.

OEBO SCHEDULE 1

LIST OF PROPOSED CONTRACTOR/CONSULTANT AND SUBCONTRACTOR/SUBCONSULTANT PARTICIPATION

FIS & Building 846 Storm Resiliency Modifications Package 2

SOLICITATION/PROJECT/BID NAME:

SOLICITATION/PROJECT/BID No.: 

DOA 18-13 (SL-04)

NAME OF PRIME RESPONDENT/BIDDER: 

Lebolo Construction Management, Inc

ADDRESS: 

2100 Corporate Drive, Boynton Beach, FL 33426

CONTACT PERSON: 

Sebastian Fonnegra

PHONE NO.: 

(561) 742 7644

SOLICITATION OPENING/SUBMITTAL DATE: 

N/A

E-MAIL: 

sfonnegra@lebolo.com

DEPARTMENT: 

PreConstruction

PLEASE LIST THE DOLLAR AMOUNT OR PERCENTAGE OF WORK TO BE COMPLETED BY THE PRIME CONTRACTOR/CONSULTANT ON THIS PROJECT.  
PLEASE ALSO LIST THE DOLLAR AMOUNT OR PERCENTAGE OF WORK TO BE COMPLETED BY ALL SUBCONTRACTORS/SUBCONSULTANTS ON THE PROJECT.

(Check all Applicable Categories)						DOLLAR AMOUNT OR PERCENTAGE OF WORK					
Name, Address and Phone Number	Non-SBE		M/WBE		SBE		Black	Hispanic	Women	Caucasian	Other (Please Specify)
			Minority/Women Business		Small Business						
1. Protect Video	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>			\$33,600.00			
2. Bonded Lightning	<input checked="" type="checkbox"/>		<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>					\$5,100.00	
3.	<input type="checkbox"/>		<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>						
4.	<input type="checkbox"/>		<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>						
5.	<input type="checkbox"/>		<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>						

(Please use additional sheets if necessary)

Total

\$637,296.64

\$33,600.00

\$39,750.00

\$251,562.64

Total Bid Price \$

\$1,518,790.48

Total SBE - M/WBE Participation

\$921,435

I hereby certify that the above information is accurate to the best of my knowledge:

Signature

PreConstruction Manager

Title

Note: 1. The amount listed on this form for a Subcontractor/subconsultant must be supported by price or percentage listed on the properly executed Schedule 2 or attached signed proposal.  
2. Firms may be certified by Palm Beach County as an SBE and/or an M/WBE. If firms are certified as both an SBE and/or M/WBE, please indicate the dollar amount under the appropriate category.  
3. Modification of this form is not permitted and will be rejected upon submittal.



OEBO LETTER OF INTENT – SCHEDULE 2

A completed Schedule 2 is a binding document between the Prime Contractor/consultant and a Subcontractor/subconsultant (for any tier) and should be treated as such. The Schedule 2 shall contain bolded language indicating that by signing the Schedule 2, both parties recognize this Schedule as a binding document. All subcontractors/subconsultants, including any tiered subcontractors/subconsultants, must properly execute this document. Each properly executed Schedule 2 must be submitted with the bid/proposal.

SOLICITATION/PROJECT NUMBER: DOA 18-13 (SL-04)

SOLICITATION/PROJECT NAME: FIS & Building 846 Storm Resiliency Modifications Package 2

Name of Prime: Lebolo Construction Management, Inc

(Check box(s) that apply)

☐SBE ☐ WBE ☐ MBE ☐ M/WBE ☒ Non-S/M/WBE Date of Palm Beach County Certification (if applicable):

The undersigned affirms they are the following (select one from each column):

Column 1

Column 2

☒ Male ☐ Female ☐ African-American/Black ☐ Asian American ☒ Caucasian American ☐ Hispanic American ☐ Native American

S/M/WBE PARTICIPATION – S/M/WBE Primes must document all work to be performed by their own work force on this form. Failure to submit a properly executed Schedule 2 for any S/M/WBE participation may result in that participation not being counted. Specify in detail, the scope of work to be performed or items supplied with the dollar amount and/or percentage for each work item. S/M/WBE credit will only be given for the areas in which the S/M/WBE is certified. A detailed proposal may be attached to a properly executed Schedule 2.

Line Item	Item Description	Unit Price	Qty./Units	Contingencies/ Allowances	Total Price/Percentage
1.0	Remove and Replace Acoustical Ceilings	\$31,988.04	1	\$ 0.00	\$31,988.04


The undersigned Subcontractor/subconsultant is prepared to self-perform the above-described work in conjunction with the aforementioned project at the following total price or percentage: \$31,988.04

If the undersigned intends to subcontract any portion of this work to another Subcontractor/subconsultant, please list the business name and the amount below accompanied by a separate properly executed Schedule 2.

Name of 2<sup>nd</sup>/3<sup>rd</sup> tier Subcontractor/subconsultant

Price or Percentage:

Lebolo Construction Management, Inc  
Print name of Prime


By:   
Authorized Signature

Sebastian Fonnegra  
Print name

PreConstruction Manager  
Title

Date: March 21, 2022

All American Ceilings  
Print name of Subcontractor/subconsultant

By:   
Authorized Signature

Robert Rawiszer  
Print name

President  
Title

Date: March 21, 2022

OEBO LETTER OF INTENT – SCHEDULE 2

A completed Schedule 2 is a binding document between the Prime Contractor/consultant and a Subcontractor/subconsultant (for any tier) and should be treated as such. The Schedule 2 shall contain bolded language indicating that by signing the Schedule 2, both parties recognize this Schedule as a binding document. All subcontractors/subconsultants, including any tiered subcontractors/subconsultants, must properly execute this document. Each properly executed Schedule 2 must be submitted with the bid/proposal.

SOLICITATION/PROJECT NUMBER: DOA 18-13 (SL-04)

SOLICITATION/PROJECT NAME: FIS & Building 846 Storm Resiliency Modifications Package 2

Name of Prime: Lebolo Construction Management, Inc

(Check box(s) that apply)

☒SBE ☐WBE ☐MBE ☐M/WBE ☐Non-S/M/WBE Date of Palm Beach County Certification (if applicable):

The undersigned affirms they are the following (select one from each column):

Column 1

Column 2

☒Male ☐Female

☐African-American/Black ☐Asian American ☒Caucasian American

☐Hispanic American ☐Native American

**S/M/WBE PARTICIPATION** – S/M/WBE Primes must document all work to be performed by their own work force on this form. Failure to submit a properly executed Schedule 2 for any S/M/WBE participation may result in that participation not being counted. Specify in detail, the scope of work to be performed or items supplied with the dollar amount and/or percentage for each work item. S/M/WBE credit will only be given for the areas in which the S/M/WBE is certified. A detailed proposal may be attached to a properly executed Schedule 2.

Line Item	Item Description	Unit Price	Qty./Units	Contingencies/ Allowances	Total Price/Percentage
1.0	Structural Steel & Misc. Metals Package	\$210,788.50	1	\$ 0.00	\$210,788.50

The undersigned Subcontractor/subconsultant is prepared to self-perform the above-described work in conjunction with the aforementioned project at the following total price or percentage: \$210,788.50

If the undersigned intends to subcontract any portion of this work to another Subcontractor/subconsultant, please list the business name and the amount below accompanied by a separate properly executed Schedule 2.

Name of 2<sup>nd</sup>/3<sup>rd</sup> tier Subcontractor/subconsultant

Price or Percentage:

Lebolo Construction Management, Inc

Print name of Prime

By:

Authorized Signature

Sebastian Fonnegra

Print name

PreConstruction Manager

Title

Date:

3/21/2022

Van Linda Iron Works, Inc.

Print name of Subcontractor/subconsultant

By:

Authorized Signature

Steven McBrearty

Print name

Director of Estimating and Project Management

Title

Date:

03/21/2022

Revised 12/31/2018



## OEBO LETTER OF INTENT – SCHEDULE 2

A completed Schedule 2 is a binding document between the Prime Contractor/consultant and a Subcontractor/subconsultant (for any tier) and should be treated as such. The Schedule 2 shall contain bolded language indicating that by signing the Schedule 2, both parties recognize this Schedule as a binding document. All subcontractors/subconsultants, including any tiered subcontractors/subconsultants, must properly execute this document. Each properly executed Schedule 2 must be submitted with the bid/proposal.

SOLICITATION/PROJECT NUMBER: DOA 18-13 (SL-04)

SOLICITATION/PROJECT NAME: FIS & Building 846 Storm Resiliency Modifications Package 2

Name of Prime: Lebolo Construction Management, Inc

**(Check box(s) that apply)**

☒ SBE ☐ WBE ☐ MBE ☒ M/WBE ☐ Non-S/M/WBE Date of Palm Beach County Certification (if applicable): \_\_\_\_\_

The undersigned affirms they are the following (select one from each column):

**Column 1**

**Column 2**

☐ Male ☒ Female

☐ African-American/Black ☐ Asian American ☐ Caucasian American

☒ Hispanic American ☐ Native American

**S/M/WBE PARTICIPATION** – S/M/WBE Primes must document all work to be performed by their own work force on this form. Failure to submit a properly executed Schedule 2 for any S/M/WBE participation may result in that participation not being counted. Specify in detail, the scope of work to be performed or items supplied with the dollar amount and/or percentage for each work item. S/M/WBE credit will only be given for the areas in which the S/M/WBE is certified. A detailed proposal may be attached to a properly executed Schedule 2.

Line Item	Item Description	Unit Price	Qty./Units	Contingencies/ Allowances	Total Price/Percentage
1.0	Drywall Ceilings & Painting Package	\$39,750.00	1	\$ 0.00	\$39,750.00

The undersigned Subcontractor/subconsultant is prepared to self-perform the above-described work in conjunction with the aforementioned project at the following total price or percentage: \$39,750.00

If the undersigned intends to subcontract any portion of this work to another Subcontractor/subconsultant, please list the business name and the amount below accompanied by a separate properly executed Schedule 2.

Name of 2<sup>nd</sup>/3<sup>rd</sup> tier Subcontractor/subconsultant

Price or Percentage: \_\_\_\_\_

Lebolo Construction Management, Inc

Print name of Prime

By: \_\_\_\_\_

Authorized Signature

Sebastian Fonnegra

Print name

PreConstruction Manager

Title

Date: 3/21/22

I.Q. Constructions

Print name of Subcontractor/subconsultant

By: \_\_\_\_\_

Authorized Signature

Print name

Owner - Qualifier

Title

Date: 3.21.22

Revised 12/31/2018

OEBO LETTER OF INTENT – SCHEDULE 2

A completed Schedule 2 is a binding document between the Prime Contractor/consultant and a Subcontractor/subconsultant (for any tier) and should be treated as such. The Schedule 2 shall contain bolded language indicating that by signing the Schedule 2, both parties recognize this Schedule as a binding document. All subcontractors/subconsultants, including any tiered subcontractors/subconsultants, must properly execute this document. Each properly executed Schedule 2 must be submitted with the bid/proposal.

SOLICITATION/PROJECT NUMBER: DOA 18-13 (SL-04)

SOLICITATION/PROJECT NAME: FIS & Building 846 Storm Resiliency Modifications Package 2

Name of Prime: Lebolo Construction Management, Inc

(Check box(s) that apply)

☐SBE ☐WBE ☐MBE ☐M/WBE ☒Non-S/M/WBE Date of Palm Beach County Certification (if applicable):

The undersigned affirms they are the following (select one from each column):

Column 1

Column 2

☐Male ☐Female ☐African-American/Black ☐Asian American ☐Caucasian American  
☐Hispanic American ☐Native American

S/M/WBE PARTICIPATION – S/M/WBE Primes must document all work to be performed by their own work force on this form. Failure to submit a properly executed Schedule 2 for any S/M/WBE participation may result in that participation not being counted. Specify in detail, the scope of work to be performed or items supplied with the dollar amount and/or percentage for each work item. S/M/WBE credit will only be given for the areas in which the S/M/WBE is certified. A detailed proposal may be attached to a properly executed Schedule 2.

Line Item	Item Description	Unit Price	Qty./Units	Contingencies/ Allowances	Total Price/Percentage
1.0	Fire Protection Package	\$3,685.83	1	\$ 0.00	\$3,685.83

The undersigned Subcontractor/subconsultant is prepared to self-perform the above-described work in conjunction with the aforementioned project at the following total price or percentage: \$3,685.83

If the undersigned intends to subcontract any portion of this work to another Subcontractor/subconsultant, please list the business name and the amount below accompanied by a separate properly executed Schedule 2.

Name of 2<sup>nd</sup>/3<sup>rd</sup> tier Subcontractor/subconsultant

Price or Percentage:

Lebolo Construction Management, Inc

Print name of Prime

By: 

Authorized Signature

Sebastian Fonnegra

Print name

PreConstruction Manager

Title

Date: 03/21/22

Johnson's Controls

Print name of Subcontractor/subconsultant

By: Brian J. Grabenhorst Digitally signed by Brian J. Grabenhorst  
Date: 2022.03.22 14:44:51 -04'00'

Authorized Signature

Brian Grabenhorst

Print name

Sprinkler Install Manager

Title

Date: March 22nd, 2022

OEBO LETTER OF INTENT – SCHEDULE 2

A completed Schedule 2 is a binding document between the Prime Contractor/consultant and a Subcontractor/subconsultant (or any tier) and should be treated as such. The Schedule 2 shall contain bolded language indicating that by signing the Schedule 2, both parties recognize this Schedule as a binding document. All subcontractors/subconsultants, including any tiered subcontractors/subconsultants, must properly execute this document. Each properly executed Schedule 2 must be submitted with the bid/proposal.

SOLICITATION/PROJECT NUMBER: DOA 18-13 (SL-04)

SOLICITATION/PROJECT NAME: FIS & Building 846 Storm Resiliency Modifications Package 2

Name of Prime: Lebolo Construction Management, Inc

(Check box(s) that apply)

☒SBE ☐WBE ☒MBE ☐M/WBE ☐Non-S/M/WBE Date of Palm Beach County Certification (if applicable): 09/30/2020

The undersigned affirms they are the following (select one from each column):

Column 1

Column 2

☒Male ☐Female ☒African-American/Black ☐Asian American ☐Caucasian American  
☐Hispanic American ☐Native American

**S/M/WBE PARTICIPATION** – S/M/WBE Primes must document all work to be performed by their own work force on this form. Failure to submit a properly executed Schedule 2 for any S/M/WBE participation may result in that participation not being counted. Specify in detail, the scope of work to be performed or items supplied with the dollar amount and/or percentage for each work item. S/M/WBE credit will only be given for the areas in which the S/M/WBE is certified. A detailed proposal may be attached to a properly executed Schedule 2.

Line Item	Item Description	Unit Price	Qty./Units	Contingencies/ Allowances	Total Price/Percentage
1.0	HVAC Package	\$577,320.00	1	\$ 0.00	\$577,320.00
2.0	HVAC Duct Cleaning	\$59,976.00	1	\$0.00	\$59,976.00

The undersigned Subcontractor/subconsultant is prepared to self-perform the above-described work in conjunction with the aforementioned project at the following total price or percentage: \$637,296.00


If the undersigned intends to subcontract any portion of this work to another Subcontractor/subconsultant, please list the business name and the amount below accompanied by a separate properly executed Schedule 2.

Name of 2<sup>nd</sup>/3<sup>rd</sup> tier Subcontractor/subconsultant

Price or Percentage:

Lebolo Construction Management, Inc

Print name of Prime

By: 

Authorized Signature

Sebastian Fonnegra

Print name


PreConstruction Manager

Title

Date: 03/21/22

Quantum Mechanical

Print name of Subcontractor/subconsultant

By: 

Authorized Signature

Patrick N. Gordon

Print name

President

Title

Date: 03/22/22



OEBO LETTER OF INTENT – SCHEDULE 2

A completed Schedule 2 is a binding document between the Prime Contractor/consultant and a Subcontractor/subconsultant (for any tier) and should be treated as such. The Schedule 2 shall contain bolded language indicating that by signing the Schedule 2, both parties recognize this Schedule as a binding document. All subcontractors/subconsultants, including any tiered subcontractors/subconsultants, must properly execute this document. Each properly executed Schedule 2 must be submitted with the bid/proposal.

SOLICITATION/PROJECT NUMBER: DOA 18-13 (SL-04)

SOLICITATION/PROJECT NAME: FIS & Building 846 Storm Resiliency Modifications Package 2

Name of Prime: Lebolo Construction Management, Inc

(Check box(s) that apply)

☒SBE ☐ WBE ☐ MBE ☒M/WBE ☐Non-S/M/WBE Date of Palm Beach County Certification (if applicable):

The undersigned affirms they are the following (select one from each column):

Column 1

Column 2

☐Male ☒Female ☐African-American/Black ☐Asian American ☐Caucasian American ☒Hispanic American ☐Native American

S/M/WBE PARTICIPATION – S/M/WBE Primes must document all work to be performed by their own work force on this form. Failure to submit a properly executed Schedule 2 for any S/M/WBE participation may result in that participation not being counted. Specify in detail, the scope of work to be performed or items supplied with the dollar amount and/or percentage for each work item. S/M/WBE credit will only be given for the areas in which the S/M/WBE is certified. A detailed proposal may be attached to a properly executed Schedule 2.

Line Item	Item Description	Unit Price	Qty./Units	Contingencies/ Allowances	Total Price/Percentage
1.0	Electrical Package	\$33,600.00	1	\$ 0.00	\$33,600.00

The undersigned Subcontractor/subconsultant is prepared to self-perform the above-described work in conjunction with the aforementioned project at the following total price or percentage: \$33,600.00


If the undersigned intends to subcontract any portion of this work to another Subcontractor/subconsultant, please list the business name and the amount below accompanied by a separate properly executed Schedule 2.

Name of 2<sup>nd</sup>/3<sup>rd</sup> tier Subcontractor/subconsultant

Price or Percentage:

Lebolo Construction Management, Inc

Print name of Prime

By: 

Authorized Signature

Sebastian Fonnegra

Print name

PreConstruction Manager

Title

Date: 03/21/22

Protect Video

Print name of Subcontractor/subconsultant

By: 

Authorized Signature

Shad DiMaria

Print name

President

Title

Date: 03/21/22

OEBO LETTER OF INTENT – SCHEDULE 2

A completed Schedule 2 is a binding document between the Prime Contractor/consultant and a Subcontractor/subconsultant (for any tier) and should be treated as such. The Schedule 2 shall contain bolded language indicating that by signing the Schedule 2, both parties recognize this Schedule as a binding document. All subcontractors/subconsultants, including any tiered subcontractors/subconsultants, must properly execute this document. Each properly executed Schedule 2 must be submitted with the bid/proposal.

SOLICITATION/PROJECT NUMBER: DOA 18-13 (SL-04)  
SOLICITATION/PROJECT NAME: FIS & Building 846 Storm Resiliency Modifications Package 2

Name of Prime: Lebolo Construction Management, Inc

(Check box(s) that apply)

☐SBE ☐ WBE ☐ MBE ☐ M/WBE ☒ Non-S/M/WBE Date of Palm Beach County Certification (if applicable):

The undersigned affirms they are the following (select one from each column):

Column 1

Column 2

☒ Male ☐ Female ☐ African-American/Black ☐ Asian American ☒ Caucasian American  
☐ Hispanic American ☐ Native American

S/M/WBE PARTICIPATION – S/M/WBE Primes must document all work to be performed by their own work force on this form. Failure to submit a properly executed Schedule 2 for any S/M/WBE participation may result in that participation not being counted. Specify in detail, the scope of work to be performed or items supplied with the dollar amount and/or percentage for each work item. S/M/WBE credit will only be given for the areas in which the S/M/WBE is certified. A detailed proposal may be attached to a properly executed Schedule 2.


Line Item	Item Description	Unit Price	Qty./Units	Contingencies/ Allowances	Total Price/Percentage
1.0	Lightning Package	\$5,100.00	1	\$ 0.00	\$5,100.00


The undersigned Subcontractor/subconsultant is prepared to self-perform the above-described work in conjunction with the aforementioned project at the following total price or percentage: \$5,100.00

If the undersigned intends to subcontract any portion of this work to another Subcontractor/subconsultant, please list the business name and the amount below accompanied by a separate properly executed Schedule 2.

Name of 2<sup>nd</sup>/3<sup>rd</sup> tier Subcontractor/subconsultant

Price or Percentage:

Lebolo Construction Management, Inc  
Print name of Prime  
By:   
Authorized Signature  
Sebastian Fonnegra  
Print name  
PreConstruction Manager  
Title  
Date: 03/21/22

Bonded Lightning  
Print name of Subcontractor/subconsultant  
By:   
Authorized Signature  
Patrick Dillon  
Print name  
President  
Title  
Date: 03/21/22

22-0626

BUDGET TRANSFER  
BOARD OF COUNTY COMMISSIONERS  
PALM BEACH COUNTY, FLORIDA

Page 1 of 1 pages

Advantage Document Numbers  
BGEX 032822/1444- 1100

Fund 4111 Airport Passenger Improvement and Development Fund

Use this form to provide budget for items not anticipated in the budget.

ACCT.NUMBER	ACCOUNT NAME	ADOPTED BUDGET	CURRENT BUDGET	INCREASE	DECREASE	ADJUSTED BUDGET	EXPENDED/ ENCUMBERED AS OF 03/28/2022	REMAINING BALANCE
121-A413-6505	lotb Non Infrastructure	1,000,000	1,000,000	518,791		1,518,791	0	1,518,791
121-A900-9909	Reserves Improvement Program	19,773,212	9,174,926		518,791	8,656,135	0	8,656,135
Total Appropriations & Expenditures			518,791	518,791		0		

OFMB

INITIATING DEPARTMENT/DIVISION

Administration/Budget Department Approval

By Board of County Commissioners

At Meeting of

May 3, 2022

By: *Brandonino*  
Deputy Clerk to the  
Board of County Commissioners

OFMB Department - Posted

STATE OF FLORIDA, COUNTY OF PALM BEACH

I, JOSEPH ABRUZZO, Clerk of the Circuit Court & Comptroller, certify this to be a true and correct copy of the original filed in my office.

on MAY 03 2022

dated at West Palm Beach, FL on 05/05/2022

By: *Brandonino*  
Deputy Clerk
